

Act ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2006												2007												2008											
							JAN	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
WARRENTON AQUATICS AND RECR FACILITY																																										
ASPHALT																																										
		224	224	10MAY06	28MAR07	56d																																				
1430	RTE. 211 ACCESS RD. BASE	15	15	10MAY06	31MAY06	5d																																				
1420	WATERLOO ACCESS RDS & PARKING	35	35	01JUN06	20JUL06	5d																																				
1360	WATERLOO RD. IMPROVEMENTS	15	15	21JUL06	10AUG06	48d																																				
1400	ASPHALT TRAILS	20	20	25SEP06	20OCT06	8d																																				
1380	PARKING LOT/ACCESS ROAD FINAL	10	10	15MAR07	28MAR07	56d																																				
CABLE																																										
		5	5	10MAY06	16MAY06	40d																																				
1240	FIBER-OPTIC & CABLE SERVICE TO	5	5	10MAY06	16MAY06	40d																																				
CARPENTRY																																										
		275	275	29MAR06	26APR07	6d																																				
3725	SET CMU WALL DOOR FRAMES	65	65	29MAR06	28JUN06	60d																																				
3731	HANG EXTERIOR DOORS	5	5	06NOV06	10NOV06	21d																																				
3730	HANG INTERIOR DOORS	10	10	16MAR07	29MAR07	6d																																				
3740	INSTALL DOOR HARDWARE	20	20	30MAR07	26APR07	6d																																				
COLUMBIA GAS																																										
		5	5	03MAY06	09MAY06	20d																																				
1210	GAS SERVICE TO BLDG.	5	5	03MAY06	09MAY06	20d																																				
CONCRETE																																										
		285	285	15FEB06	29MAR07	5d																																				
2110	FOOTINGS - A-B	30	30	15FEB06	28MAR06	0																																				
2130	COMP POOL PIT, TANK & CATCH BASIN	10	10	15FEB06	28FEB06	9d																																				
2120	CONC. WALLS AND COLUMNS - A	25	25	22FEB06	28MAR06	9d																																				
2010	CONC WALLS AND COLUMNS - B	25	25	15MAR06	18APR06	20d																																				
2012	LEISURE POOL PUMP PIT WALLS AND	5	5	15MAR06	21MAR06	15d																																				
2135	VESTIBULE TOWER CONCRETE	10	10	15MAR06	28MAR06	9d																																				
2020	ELEVATOR PIT WALLS AND SLAB	5	5	22MAR06	28MAR06	20d																																				
2190	SLAB ON GRADE - A & B	20	20	29MAR06	25APR06	10d																																				
2200	DECK CONCRETE - A EAST	10	10	11MAY06	24MAY06	49d																																				
2090	DECK CONCRETE - B EAST	10	10	14JUN06	27JUN06	26d																																				
2240	COMPETITION POOL DECK CONCRETE	5	5	21FEB07	27FEB07	21d																																				

**FORRESTER CONSTRUCTION COMPANY
WARRENTON AQUATICS AND RECR FACILITY**

Start date	10JAN06
Finish date	01AUG07
Data date	10JAN06
Run date	25OCT06
Page number	1A
© Primavera Systems, Inc.	

Calculate: Total
Display: Quantity
Interval: Month
Total cumulative curve

- Early start point
- Early finish point
- Early bar
- Total float bar
- Progress bar
- Critical bar
- Summary bar
- Progress point
- Critical point
- Summary point
- Start milestone point
- Finish milestone point

Act ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2006												2007												2008											
							JAN	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J					
2250	LEISURE POOL DECK CONCRETE	5	5	23MAR07	29MAR07	5d	▲▼ LEISURE POOL DECK CONCRETE																																			
DOMINION RESOURCES																																										
		160	160	05APR06	17NOV06	61d	▲▼																																			
1220	ELECTRIC & TEL. SERVICE TO BLDG.	15	15	05APR06	25APR06	20d	▲▼ ELECTRIC & TEL. SERVICE TO BLDG.																																			
1221	SET AND WIRE PERMANENT	10	10	06NOV06	17NOV06	61d	▲▼ SET AND WIRE PERMANENT TRANSFORMER																																			
DRYWALL																																										
		179	179	17JUL06	29MAR07	45d	▲▼																																			
3340	FRAME LIGHT MONITOR WINDOW	5	5	17JUL06	21JUL06	49d	▲▼ FRAME LIGHT MONITOR WINDOW OPENING, A																																			
3360	ROOF OVERBUILD, FRAME AND DECK, A	10	10	17JUL06	28JUL06	14d	▲▼ ROOF OVERBUILD, FRAME AND DECK, A																																			
3330	EXT. FURRING / SHEATHING - A NORTH	5	5	14AUG06	18AUG06	76d	▲▼ EXT. FURRING / SHEATHING - A NORTH																																			
3350	FRAME LIGHT MONITOR WINDOW	5	5	25AUG06	31AUG06	45d	▲▼ FRAME LIGHT MONITOR WINDOW OPENING, B																																			
3370	ROOF OVERBUILD, FRAME AND DECK, B	10	10	25AUG06	08SEP06	5d	▲▼ ROOF OVERBUILD, FRAME AND DECK, B																																			
3310	EXT. STUDS / SHEATHING - B SOUTH	10	10	25SEP06	06OCT06	8d	▲▼ EXT. STUDS / SHEATHING - B SOUTH																																			
3384	FRAME DRYWALL, B	15	15	30OCT06	17NOV06	47d	▲▼ FRAME DRYWALL, B																																			
3374	ACOUSTIC CEILING PANELS, COMPETITION POOL	5	5	20DEC06	27DEC06	21d	▲▼ ACOUSTIC CEILING PANELS, COMPETITION POOL																																			
3385	HANG AND FINISH DRYWALL A	45	45	05JAN07	08MAR07	37d	▲▼ HANG AND FINISH DRYWALL A																																			
3387	HANG AND FINISH DRYWALL, B	20	20	12JAN07	08FEB07	7d	▲▼ HANG AND FINISH DRYWALL, B																																			
3395	ACT GRID, B	2	2	12JAN07	15JAN07	67d	▲▼ ACT GRID, B																																			
3391	ACT GRID, A	5	5	24JAN07	30JAN07	37d	▲▼ ACT GRID, A																																			
3375	ACOUSTIC CEILING PANELS, LEISURE POOL	5	5	02FEB07	08FEB07	0	▲▼ ACOUSTIC CEILING PANELS, LEISURE POOL																																			
3372	METAL PAN CEILING GRID, UPPER LEVEL B	5	5	16FEB07	22FEB07	56d	▲▼ METAL PAN CEILING GRID, UPPER LEVEL B																																			
3373	METAL PAN CEILING PANELS, UPPER LEVEL B	5	5	09MAR07	15MAR07	46d	▲▼ METAL PAN CEILING PANELS, UPPER LEVEL B																																			
3396	ACT TILE, B	2	2	16MAR07	19MAR07	24d	▲▼ ACT TILE, B																																			
3392	ACT TILE A	8	8	20MAR07	29MAR07	45d	▲▼ ACT TILE A																																			
ELECTRICAL																																										
		352	352	08FEB06	26JUN07	20d	▲▼																																			
1060	TEMPORARY ELECTRIC	10	10	08FEB06	21FEB06	10d	▲▼ TEMPORARY ELECTRIC																																			
5560	CMU WALL ELECT ROUGH-IN	90	90	29MAR06	03AUG06	40d	▲▼ CMU WALL ELECT ROUGH-IN																																			
5520	SITE LIGHTING CONDUIT AND BASES	20	20	12APR06	09MAY06	5d	▲▼ SITE LIGHTING CONDUIT AND BASES																																			
5570	INSTALL SWITCHGEAR	10	10	21JUN06	05JUL06	83d	▲▼ INSTALL SWITCHGEAR																																			
5540	SITE LIGHT POLES	5	5	21JUL06	27JUL06	202d	▲▼ SITE LIGHT POLES																																			
5500	ELEC. CEILING ROUGH-IN, COMPETITION POOL	5	5	26SEP06	02OCT06	50d	▲▼ ELEC. CEILING ROUGH-IN, COMPETITION POOL																																			
5670	PENTHOUSE 1 LIGHTS	3	3	31OCT06	02NOV06	158d	▲▼ PENTHOUSE 1 LIGHTS																																			
5535	SET AND WIRE EMERGENCY GENERATOR	5	5	06NOV06	10NOV06	151d	▲▼ SET AND WIRE EMERGENCY GENERATOR																																			

**FORRESTER CONSTRUCTION COMPANY
WARRENTON AQUATICS AND RECR FACILITY**

Start date	10JAN06
Finish date	01AUG07
Data date	10JAN06
Run date	25OCT06
Page number	2A
© Primavera Systems, Inc.	

Calculate: Total
Display: Quantity
Interval: Month
Total cumulative curve

- ▲ Early start point
- ▼ Early finish point
- ▲▼ Early bar
- ▲▼ Total float bar
- ▲▼ Progress bar
- ▲▼ Critical bar
- ▲▼ Summary bar
- ▲ Progress point
- ▼ Critical point
- ▲▼ Summary point
- ▲ Start milestone point
- ▼ Finish milestone point

Act ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2006												2007												2008											
							JAN	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
5590	ELEC. ROUGH-IN, B, UPPER LEVEL	5	5	06NOV06	10NOV06	47d																																				
5510	ELEC. CEILING ROUGH-IN, LEISURE	5	5	14NOV06	20NOV06	24d																																				
5680	PENTHOUSE 2 LIGHTS	3	3	29NOV06	01DEC06	139d																																				
5580	ELEC. ROUGH-IN, A, UPPER LEVEL	10	10	12JAN07	25JAN07	16d																																				
5610	LIGHTS / DEVICES	35	35	07FEB07	27MAR07	84d																																				
5600	FIRE ALARM	60	60	23FEB07	17MAY07	22d																																				
5551	FIRE ALARM/SPRINKLER FINAL	5	5	20JUN07	26JUN07	0																																				
ELEVATOR																																										
		236	236	04APR06	08MAR07	72d																																				
2002	DRILL ELEVATOR JACK HOLE	5	5	04APR06	10APR06	21d																																				
2003	INSTALL ELEVATOR EQUIPMENT	5	5	05JAN07	11JAN07	72d																																				
2004	INSTALL ELEVATOR RAILS	5	5	12JAN07	18JAN07	72d																																				
2005	BUILD ELEVATOR PLATFORM	5	5	19JAN07	25JAN07	72d																																				
2006	ELEVATOR DOOR FRAMES	5	5	26JAN07	01FEB07	72d																																				
2007	ELEVATOR DOORS HATCHWORK/CAB	10	20	09FEB07	08MAR07	72d																																				
EXCAVATION																																										
		160	160	18JAN06	31AUG06	0																																				
1040	EROSION CONTROLS	10	10	18JAN06	31JAN06	0																																				
1300	ROUGH GRADE SITE	40	40	01FEB06	28MAR06	0																																				
1310	FOREBAY EXCAVATION AND LINER	30	30	29MAR06	09MAY06	25d																																				
1550	BACKFILL NORTH FOUNDATION WALL	5	5	03MAY06	09MAY06	55d																																				
1551	BACKFILL EAST FOUNDATION WALL	15	15	29JUN06	20JUL06	25d																																				
1560	SPREAD TOPSOIL	25	25	28JUL06	31AUG06	0																																				
FIRE PROTECTION																																										
		140	140	25AUG06	15MAR07	15d																																				
5820	SPRINKLERS, A	40	40	25AUG06	20OCT06	115d																																				
5830	SPRINKLERS, B	27	27	25SEP06	31OCT06	52d																																				
5800	SPRINKLERS, COMPETITION POOL	10	10	19JAN07	01FEB07	21d																																				
5810	SPRINKLERS, LEISURE POOL	10	10	02MAR07	15MAR07	0																																				
FLOOR COVERINGS																																										
		15	15	27APR07	17MAY07	6d																																				
9050	CARPET AND BASE, UPPER LEVEL A	10	10	27APR07	10MAY07	6d																																				
9051	RUBBER FLOOR, MULTI PURPOSE AND	5	5	11MAY07	17MAY07	6d																																				

**FORRESTER CONSTRUCTION COMPANY
WARRENTON AQUATICS AND RECR FACILITY**

Start date	10JAN06	Calculate: Total	Early start point
Finish date	01AUG07		
Data date	10JAN06	Interval: Month	Total float point
Run date	25OCT06		
Page number	3A	Progress bar	Critical bar
		Critical point	Summary point
© Primavera Systems, Inc.			

Act ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2006												2007												2008											
							JAN	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J					
		398	398	10JAN06	01AUG07	0	[Gantt bar for total project duration]																																			
1010	MOBILIZE	10	10	10JAN06	23JAN06	0	MOBILIZE																																			
3603	BUILDING WATERTIGHT	0	0		04JAN07	7d	BUILDING WATERTIGHT																																			
1006	FINAL SITE INSPECTION	5	5	07MAY07	11MAY07	31d	FINAL SITE INSPECTION																																			
1016	FINAL CLEAN	15	15	30MAY07	19JUN07	0	FINAL CLEAN																																			
1011	FINAL BLD. INSP./ BLD. PERFORMANCE	5	5	27JUN07	03JUL07	0	FINAL BLD. INSP./ BLD. PERFORMANCE																																			
1012	CERTIFICATE OF OCCUPANCY/SUB.	0	0		03JUL07	0	CERTIFICATE OF OCCUPANCY/SUB.																																			
1014	PUNCHLIST	20	20	05JUL07	01AUG07	0	PUNCHLIST																																			
1015	FINAL COMPLETION	0	0		01AUG07	0	FINAL COMPLETION																																			
GLASS AND GLAZING																																										
		202	202	24JUL06	08MAY07	7d	[Gantt bar for glass and glazing summary]																																			
3660	LIGHT MONITOR GLAZING, A	10	10	24JUL06	04AUG06	49d	LIGHT MONITOR GLAZING, A																																			
3670	LIGHT MONITOR GLAZING, B	10	10	01SEP06	15SEP06	45d	LIGHT MONITOR GLAZING, B																																			
3610	EXTERIOR STOREFRONT - BLDG A	20	20	16OCT06	10NOV06	21d	EXTERIOR STOREFRONT - BLDG A																																			
3600	EXTERIOR STOREFRONT - BLDG. B	20	20	06NOV06	05DEC06	0	EXTERIOR STOREFRONT - BLDG. B																																			
3620	INTERIOR STOREFRONT, A	5	15	12JAN07	01FEB07	26d	INTERIOR STOREFRONT, A																																			
3640	INTERIOR STOREFRONT, B	10	10	23FEB07	08MAR07	46d	INTERIOR STOREFRONT, B																																			
3651	MULTI-PURPOSE AND FITNESS ROOM	2	2	07MAY07	08MAY07	7d	MULTI-PURPOSE AND FITNESS ROOM MIF																																			
MECHANICAL HVAC																																										
		216	216	04AUG06	11JUN07	21d	[Gantt bar for mechanical hvac summary]																																			
5080	DUCT, A	30	30	04AUG06	15SEP06	71d	DUCT, A																																			
5010	PENTHOUSE 1 DUCT	35	35	28AUG06	16OCT06	86d	PENTHOUSE 1 DUCT																																			
5100	DUCT, B	30	30	01SEP06	13OCT06	47d	DUCT, B																																			
5020	PENTHOUSE 1 MECHANICAL	5	5	26SEP06	02OCT06	86d	PENTHOUSE 1 MECHANICAL EQUIPMENT																																			
5300	CONTROLS, A	90	90	03OCT06	09FEB07	86d	CONTROLS, A																																			
5050	PENTHOUSE 2 DUCT	35	35	09OCT06	28NOV06	57d	PENTHOUSE 2 DUCT																																			
5060	PENTHOUSE 2 MECHANICAL	5	5	06NOV06	10NOV06	57d	PENTHOUSE 2 MECHANICAL EQUIPMENT																																			
5200	HVAC PIPING, A	60	60	06NOV06	01FEB07	62d	HVAC PIPING, A																																			
5205	SET CHILLER CH-1	1	1	06NOV06	06NOV06	61d	SET CHILLER CH-1																																			
5310	CONTROLS, B	90	90	13NOV06	22MAR07	57d	CONTROLS, B																																			
5065	SET AND PIPE BOILERS	60	60	06DEC06	01MAR07	72d	SET AND PIPE BOILERS																																			
5210	HVAC PIPING, B	60	60	06DEC06	01MAR07	42d	HVAC PIPING, B																																			
5000	COMPETITION POOL DUCT	15	15	28DEC06	18JAN07	21d	COMPETITION POOL DUCT																																			
5320	STARTUP PENTHOUSE 1 EQUIPMENT	10	10	19JAN07	01FEB07	21d	STARTUP PENTHOUSE 1 EQUIPMENT																																			
5340	TEST AND BALANCE, A & COMP DUCT	30	30	02FEB07	15MAR07	62d	TEST AND BALANCE, A & COMP DUCT																																			

**FORRESTER CONSTRUCTION COMPANY
WARRENTON AQUATICS AND RECR FACILITY**

Start date 10JAN06
 Finish date 01AUG07
 Data date 10JAN06
 Run date 25OCT06
 Page number 4A

Calculate: Total
 Display: Quantity
 Interval: Month
 Total cumulative curve

- ▲ Early start point
- ▼ Early finish point
- █ Total float bar
- ▬ Progress bar
- ▬ Critical bar
- ▬ Summary bar
- ▲ Progress point
- ▼ Critical point
- ▲ Summary point
- ◆ Start milestone point
- ◆ Finish milestone point

Act ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2006												2007												2008											
							JAN	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J					
5040	LEISURE POOL DUCT	15	15	09FEB07	01MAR07	0	▲ LEISURE POOL DUCT																																			
5330	STARTUP PENTHOUSE 2 EQUIPMENT	10	10	02MAR07	15MAR07	5d	▲ STARTUP PENTHOUSE 2 EQUIPMENT																																			
5350	TEST AND BALANCE, B & LEISURE DUCT	30	30	16MAR07	26APR07	32d	▲ TEST AND BALANCE, B & LEISURE DUCT																																			
5360	COMMISSION HVAC SYSTEMS	20	20	14MAY07	11JUN07	21d	▲ COMMISSION HVAC SYSTEMS																																			
LANDSCAPING																																										
		136	136	30OCT06	11MAY07	31d	▲ LANDSCAPING																																			
1480	WOOD CHIP TRAIL	5	5	30OCT06	03NOV06	17d	▲ WOOD CHIP TRAIL																																			
1490	SITE	30	30	02APR07	11MAY07	31d	▲ SITE LANDSCAPING/FURNISHING/SIG																																			
LOUVERS																																										
		34	34	17JUL06	31AUG06	92d	▲ LOUVERS																																			
3710	LOUVERS - A	5	5	17JUL06	21JUL06	121d	▲ LOUVERS - A																																			
3700	LOUVERS - B	5	5	25AUG06	31AUG06	92d	▲ LOUVERS - B																																			
MASONRY																																										
		160	160	29MAR06	10NOV06	42d	▲ MASONRY																																			
2035	STAIR S-2 CMU TOWER	10	10	29MAR06	11APR06	29d	▲ STAIR S-2 CMU TOWER																																			
7050	EXTERIOR CMU BACKUP	70	70	29MAR06	03AUG06	0	▲ EXTERIOR CMU BACKUP																																			
7010	INTERIOR CMU WALLS, LOWER LVL	50	50	22JUN06	31AUG06	47d	▲ INTERIOR CMU WALLS, LOWER LVL																																			
3110	STONE / BRICK VENEER	79	79	17JUL06	03NOV06	9d	▲ STONE / BRICK VENEER																																			
3601	EXTERIOR MASONRY CAULKING	5	5	06NOV06	10NOV06	42d	▲ EXTERIOR MASONRY CAULKING																																			
MISCELLANEOUS METALS																																										
		189	189	09JUN06	08MAR07	72d	▲ MISCELLANEOUS METALS																																			
2152	INSTALL STAIR 1 AND HANDRAIL	3	3	09JUN06	13JUN06	26d	▲ INSTALL STAIR 1 AND HANDRAIL																																			
2151	INSTALL STAIR 2 AND HANDRAIL	5	5	14JUN06	20JUN06	46d	▲ INSTALL STAIR 2 AND HANDRAIL																																			
2156	MOVEABLE PARTITION SUPPORT STEEL	2	2	06JUL06	07JUL06	101d	▲ MOVEABLE PARTITION SUPPORT STEEL																																			
2153	INSTALL EXTERIOR STAIR AND	3	3	25SEP06	27SEP06	169d	▲ INSTALL EXTERIOR STAIR AND																																			
2155	SPECTATOR SEATING/GLASS HANDRAIL	20	20	09FEB07	08MAR07	52d	▲ SPECTATOR SEATING/GLASS HANDRAIL																																			
2154	INSTALL ELEVATOR PIT LADDER	1	1	23FEB07	23FEB07	81d	▲ INSTALL ELEVATOR PIT LADDER																																			
MILLWORK																																										
		24	24	23MAR07	25APR07	24d	▲ MILLWORK																																			
9153	FINISHING MILLWORK	18	18	23MAR07	17APR07	25d	▲ FINISHING MILLWORK																																			
9156	POSTER CASES/STORAGE SHELVING	2	2	24APR07	25APR07	24d	▲ POSTER CASES/STORAGE SHELVING																																			
METAL SIDING																																										
		39	39	12SEP06	03NOV06	57d	▲ METAL SIDING																																			

**FORRESTER CONSTRUCTION COMPANY
WARRENTON AQUATICS AND RECR FACILITY**

Start date 10JAN06
 Finish date 01AUG07
 Data date 10JAN06
 Run date 25OCT06
 Page number 5A
 © Primavera Systems, Inc.

Calculate: Total
 Display: Quantity
 Interval: Month
 — Total cumulative curve

- ▲ Early start point
- ▼ Early finish point
- Early bar
- ▼ Total float point
- Total float bar
- Progress bar
- Critical bar
- Summary bar
- ▲ Progress point
- ▲ Critical point
- ▲ Summary point
- ▲ Start milestone point
- ▲ Finish milestone point

Act ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2006												2007												2008											
							JAN	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J					
3430	METAL SIDING - A	20	20	12SEP06	09OCT06	76d	▲▼ METAL SIDING - A																																			
3410	METAL SIDING - B	20	20	09OCT06	03NOV06	8d	▲▼ METAL SIDING - B																																			
OWNER																																										
		0	0	10JAN06	10JAN06		▲																																			
1000	NOTICE TO PROCEED	0	0	10JAN06			◆ NOTICE TO PROCEED																																			
PAINT																																										
		105	105	13NOV06	12APR07	32d	▲▼																																			
6000	PAINT COMPETITION POOL AREA	40	40	13NOV06	11JAN07	21d	▲▼ PAINT COMPETITION POOL AREA																																			
6050	PAINT, B	30	30	20DEC06	01FEB07	12d	▲▼ PAINT, B																																			
6010	PAINT LEISURE POOL AREA	40	40	28DEC06	22FEB07	0	▲▼ PAINT LEISURE POOL AREA																																			
6040	PAINT, A	35	35	10JAN07	27FEB07	37d	▲▼ PAINT, A																																			
6100	PAINT PENTHOUSES	20	20	16MAR07	12APR07	32d	▲▼ PAINT PENTHOUSES																																			
PLUMBING																																										
		285	285	08MAR06	19APR07	25d	▲▼																																			
2013	INSTALL SEWER EJECTOR BASIN #2	5	5	08MAR06	14MAR06	15d	▲▼ INSTALL SEWER EJECTOR BASIN #2																																			
8000	UNDERGROUND PLUMBING ROUGH-IN, A	20	20	15MAR06	11APR06	10d	▲▼ UNDERGROUND PLUMBING ROUGH-IN, A EAST																																			
8020	DWV ROUGH-IN	53	53	11MAY06	26JUL06	76d	▲▼ DWV ROUGH-IN																																			
8050	UNDERGROUND PLUMBING ROUGH-IN, A	5	5	19SEP06	25SEP06	118d	▲▼ UNDERGROUND PLUMBING ROUGH-IN, COMP P																																			
8060	UNDERGROUND PLUMB ROUGH-IN, A	5	5	14NOV06	20NOV06	84d	▲▼ UNDERGROUND PLUMB ROUGH-IN, LEISURE PO																																			
8090	INST. PLUMBING FIXTURES/TOILET	15	15	30MAR07	19APR07	25d	▲▼ INST. PLUMBING FIXTURES/TOILET ACCE																																			
POOLS																																										
		236	236	17JUL06	19JUN07	5d	▲▼																																			
4100	EXCAVATE COMPETITION POOL	10	10	17JUL06	28JUL06	24d	▲▼ EXCAVATE COMPETITION POOL																																			
4110	UNDERSLAB COMPETITION POOL PIPING	10	10	31JUL06	11AUG06	24d	▲▼ UNDERSLAB COMPETITION POOL PIPING																																			
4120	COMPETITION POOL CONCRETE SHELL	15	15	14AUG06	01SEP06	24d	▲▼ COMPETITION POOL CONCRETE SHELL																																			
4000	EXCAVATE LEISURE POOL	10	10	05SEP06	18SEP06	24d	▲▼ EXCAVATE LEISURE POOL																																			
4190	BACKFILL COMPETITION POOL WALLS	5	5	12SEP06	18SEP06	55d	▲▼ BACKFILL COMPETITION POOL WALLS																																			
4005	WATERSLIDE FOOTINGS AND PIERS	5	5	19SEP06	25SEP06	34d	▲▼ WATERSLIDE FOOTINGS AND PIERS																																			
4010	UNDERSLAB LEISURE POOL PIPING	15	15	19SEP06	09OCT06	24d	▲▼ UNDERSLAB LEISURE POOL PIPING																																			
4020	LEISURE POOL CONCRETE SHELL	20	20	10OCT06	06NOV06	24d	▲▼ LEISURE POOL CONCRETE SHELL																																			
4075	COMPETITION POOL FILTER ROOM	20	20	05JAN07	01FEB07	42d	▲▼ COMPETITION POOL FILTER ROOM EQUIP																																			
4070	LEISURE POOL FILTER ROOM	20	20	02FEB07	01MAR07	42d	▲▼ LEISURE POOL FILTER ROOM EQUIPMENT																																			
4140	TILE COMP POOL INTERIOR	20	20	28FEB07	27MAR07	21d	▲▼ TILE COMP POOL INTERIOR																																			
4040	INSTALL WATERSLIDE	20	20	30MAR07	26APR07	5d	▲▼ INSTALL WATERSLIDE																																			


**FORRESTER CONSTRUCTION COMPANY
WARRENTON AQUATICS AND RECR FACILITY**

Start date 10JAN06
 Finish date 01AUG07
 Data date 10JAN06
 Run date 25OCT06
 Page number 6A

Calculate: Total
 Display: Quantity
 Interval: Month
 — Total cumulative curve


- ▲ Early start point
- ▼ Early finish point
- Early bar
- ▬ Total float bar
- ▬ Progress bar
- ▬ Critical bar
- ▬ Summary bar
- ▲ Progress point
- ▼ Critical point
- Summary point
- ◆ Start milestone point
- ◆ Finish milestone point

Act ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2006												2007												2008											
							JAN	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
4035	LEISURE POOL TILE	15	15	20APR07	10MAY07	0																																				
4150	COMP POOL PLASTER & FILL	8	8	25APR07	04MAY07	21d																																				
4045	INSTALL LEISURE POOL FEATURES	10	10	11MAY07	24MAY07	7d																																				
4048	LEISURE POOL PLASTER & FILL	12	12	11MAY07	29MAY07	0																																				
4180	STARTUP AND COMMISSION LEISURE &	10	10	30MAY07	12JUN07	0																																				
4181	FINAL HEALTH DEPT. INSPECTION	5	5	13JUN07	19JUN07	5d																																				




ROOFING

		175	175	31JUL06	06APR07	59d
3520	METAL ROOF - A EAST	20	20	31JUL06	25AUG06	14d
3500	METAL ROOF - B EAST	20	20	11SEP06	06OCT06	5d
3530	METAL ROOF - A WEST	25	25	09OCT06	10NOV06	5d
3510	METAL ROOF - B WEST	25	25	13NOV06	19DEC06	5d
3540	FLAT BUILT-UP ROOF	5	5	20DEC06	27DEC06	7d
3550	GREEN ROOF MEMBRANE	5	5	28DEC06	04JAN07	7d
3560	GREEN ROOF FILL AND PLANTS	5	5	02APR07	06APR07	59d

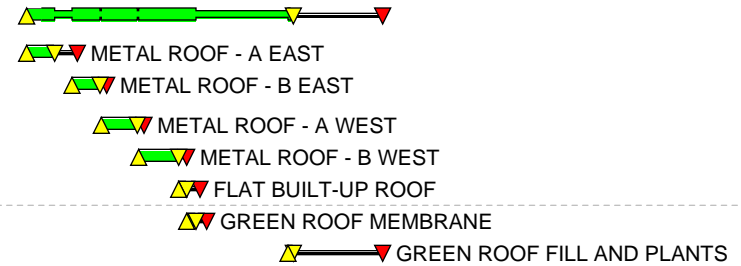


SITE CONCRETE

		261	261	17APR06	25APR07	33d
1450	CURB AND GUTTER	15	15	17APR06	05MAY06	7d
1454	ACCESS DRIVEWAY/SIDEWALKS,	20	20	01MAR07	28MAR07	33d
1452	CONCRETE PAVERS, WEST & NORTH	20	20	29MAR07	25APR07	33d




SITE UTILITIES

		73	73	08FEB06	19MAY06	42d
1190	SANITARY '1A' - '1D' - BLDG.	15	15	08FEB06	28FEB06	10d
1150	STORM 'D1' - 'D22'	13	13	01MAR06	17MAR06	20d
1100	WATER LINES 'A' & 'B'	10	10	08MAR06	21MAR06	20d
1160	STORM 'F1' - 'F10'	10	10	29MAR06	11APR06	5d
1120	STORM 'A1' - 'A2' & 'C1' - 'C2'	8	8	10MAY06	19MAY06	42d



SPECIALTY


		290	290	29MAR06	17MAY07	22d
9111	MECH AREA RETAINING WALL	15	15	29MAR06	18APR06	25d
1470	TIMBER BRIDGE	5	5	23OCT06	27OCT06	17d
9106	MECH AREA CHAIN LINK FENCE	1	1	02MAR07	02MAR07	76d
9101	INTERIOR METAL BENCHES & LOCKERS	12	12	07MAR07	22MAR07	54d
9104	TOILET PARTITIONS	5	5	23MAR07	29MAR07	25d



**FORRESTER CONSTRUCTION COMPANY
WARRENTON AQUATICS AND RECR FACILITY**

Start date 10JAN06
Finish date 01AUG07
Data date 10JAN06
Run date 25OCT06
Page number 7A

Calculate: Total
Display: Quantity
Interval: Month
Total cumulative curve



Act ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2006												2007												2008											
							JAN	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
9108	INTERIOR SIGNAGE	5	5	11MAY07	17MAY07	7d	▲▼ INTERIOR SIGNAGE																																			
STRUCTURAL STEEL																																										
		94	94	13APR06	24AUG06	0	▲▼																																			
2160	STRUCTURAL STEEL - A EAST	20	20	13APR06	10MAY06	9d	▲▼ STRUCTURAL STEEL - A EAST																																			
2050	STRUCTURAL STEEL - B EAST	20	20	11MAY06	08JUN06	9d	▲▼ STRUCTURAL STEEL - B EAST																																			
2180	ROOF DECK - A EAST	10	10	11MAY06	24MAY06	24d	▲▼ ROOF DECK - A EAST																																			
2070	ROOF DECK - B EAST	10	10	09JUN06	22JUN06	14d	▲▼ ROOF DECK - B EAST																																			
2170	STRUCTURAL STEEL - A WEST	15	15	09JUN06	29JUN06	9d	▲▼ STRUCTURAL STEEL - A WEST																																			
2185	ROOF DECK - A WEST	10	10	30JUN06	14JUL06	9d	▲▼ ROOF DECK - A WEST																																			
2060	STRUCTURAL STEEL - B WEST	10	10	21JUL06	03AUG06	0	▲▼ STRUCTURAL STEEL - B WEST																																			
2075	ROOF DECK - B WEST	15	15	04AUG06	24AUG06	0	▲▼ ROOF DECK - B WEST																																			
SURVEY																																										
		58	58	10JAN06	30MAR06	9d	▲▼																																			
1020	SITE LIMITS AND BULDING CONTROL	5	5	10JAN06	16JAN06	0	▲▼ SITE LIMITS AND BULDING CONTROL SURVEY																																			
2150	FOUNDATION SURVEY - A & B	2	2	29MAR06	30MAR06	9d	▲▼ FOUNDATION SURVEY - A & B																																			
CERAMIC TILE																																										
		43	43	12JAN07	13MAR07	37d	▲▼																																			
9002	CERAMIC TILE FLOORS, LOWER LEVEL	5	5	12JAN07	18JAN07	75d	▲▼ CERAMIC TILE FLOORS, LOWER LEVEL B																																			
9001	CERAMIC TILE FLOORS, A	25	25	07FEB07	13MAR07	37d	▲▼ CERAMIC TILE FLOORS, A																																			
WATERPROOFING																																										
		110	110	05APR06	08SEP06	25d	▲▼																																			
3280	WATERPROOF EAST & NORTH	15	15	05APR06	25APR06	67d	▲▼ WATERPROOF EAST & NORTH FOUNDATION																																			
3290	DRAIN TILE - EAST & WEST	8	8	19APR06	28APR06	67d	▲▼ DRAIN TILE - EAST & WEST																																			
3250	AIR BARRIER - A WEST	5	5	26APR06	02MAY06	60d	▲▼ AIR BARRIER - A WEST																																			
3220	AIR BARRIER - B WEST	5	5	22JUN06	28JUN06	40d	▲▼ AIR BARRIER - B WEST																																			
3265	WATERPROOF SOUTH & EAST	5	5	22JUN06	28JUN06	25d	▲▼ WATERPROOF SOUTH & EAST FOUNDATION																																			
3295	DRAIN TILE - WEST & SOUTH	5	5	26JUN06	30JUN06	26d	▲▼ DRAIN TILE - WEST & SOUTH																																			
3230	AIR BARRIER - A EAST	5	5	11AUG06	17AUG06	25d	▲▼ AIR BARRIER - A EAST																																			
3200	AIR BARRIER - B EAST	5	5	01SEP06	08SEP06	25d	▲▼ AIR BARRIER - B EAST																																			
		398	398	10JAN06	01AUG07	0	▲▼																																			

**FORRESTER CONSTRUCTION COMPANY
WARRENTON AQUATICS AND RECR FACILITY**

Start date 10JAN06
Finish date 01AUG07
Data date 10JAN06
Run date 25OCT06
Page number 8A

Calculate: Total
Display: Quantity
Interval: Month
— Total cumulative curve

- ▲ Early start point
- ▼ Early finish point
- █ Early bar
- █ Total float bar
- █ Progress bar
- █ Critical bar
- █ Summary bar
- ▲ Progress point
- ▼ Critical point
- █ Summary point
- ◆ Start milestone point
- ◆ Finish milestone point
