
Penn State Rec Hall Addition Schedule

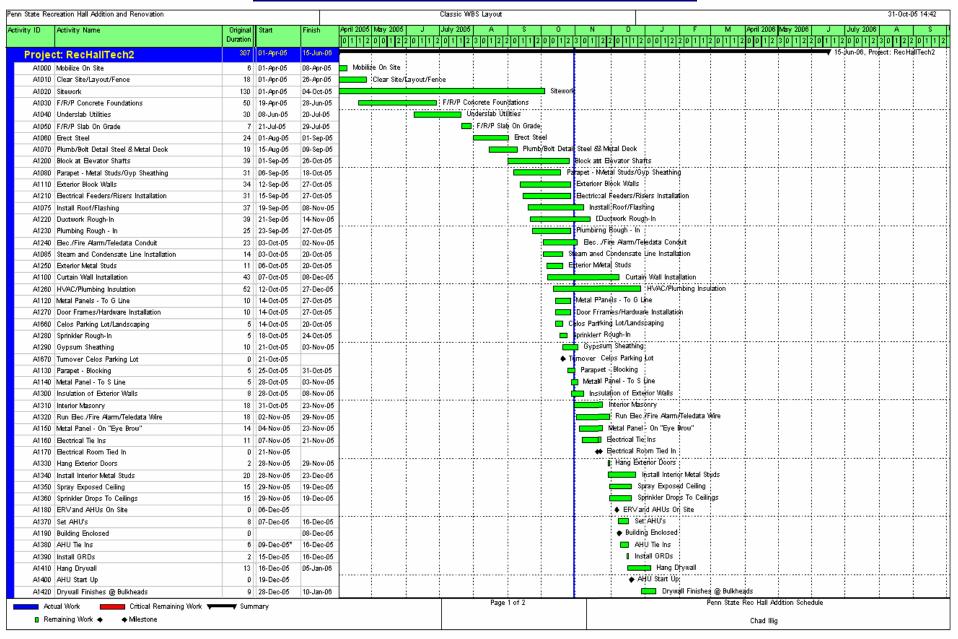

	reation Hall Addition and Renovation								lassic WBS Layout												31-Oct-05 14:46		
ity ID	Activity Name	Original Duration	Start	Finish	April 2005	May 2005	J : [0] 1] 1] 2	July 2005	A 2 0 1 2	S 	0	N 3 0 1 2 3	D 21011111	J 2 0101112	F 2 0 1 1 1	M 2 0 1 1	April 2006	May 200	6 J 22011	July 200	3 A	s	
A1440	Tape/Finish Remaining Drywall		30-Dec-05	13-Jan-06	10111112	in in in in in in	10 111112	10 1 1 2	: :	<u> </u>	10 10 1 1 12	10 10 1 1 2 1	: :	Tap	e/Finish R	emaining C)rywall	i Ialal da	15/6/11/	2 0 0 1 2	3 0 1 2	2 0 1 1	
	Lights @ High Bay	10		19-Jan-06	1				i						: ights@:H	igh Bay	1	•					
	Terrazzo Tile Installation	25	1.1	16-Feb-06												errazzo Tile	: Installation	1					
	Ceramic Tile Installation	20		09-Feb-06	+				ļ				}		Cer	amic Tile Ir	stallation	·			.		
	Painting	25		24-Feb-06	1											: :Painting							
	Accoustical Ceilings	12		14-Feb-06	1										•	coustical (Ceilings					1	
	Bec./Fire Alarm/Teledata Trim Out	20		24-Feb-06	1										-		Alarm/Tele	; data Trim	Oút				
	Resilient Flooring	20		10-Mar-06	1												ilient Floorin		T				
	Install Lights in Drop Ceiling	5	-	21-Feb-06	 	†			·				·	·}			nts in Drop (
	Test and Balance Mech. Systems		15-Feb-06	28-Feb-06	1												d Balance M		enhs				
	Set Plumbing Fixtures	8	14	01-Mar-06	1					-							mbing Fixtu						
	Install Carpet	10	-	03-Mar-06	-											install		ī					
	MEP Systems Check Out/Owner Training	20		21-Mar-06		1			:				:		1 7		MEP Syster	: rrs Check	Out/Own _{ner}	_i		1	
	Building Flush Out	10		14-Mar-06	 	<u> </u>			ļ			·	ļ	· }	. į <mark>.</mark>	Bu	ilding Flush	Aut.	ner	Training	.	.	
	Hang Interior Wood Doors	5	1	10-Mar-06	-												g Interior W		. !			1	
	Millwork	25		07-Apr-06	-												Millwo						
	Install Lockers		13-Mar-06	14-Mar-06	-	1				1						. —	tall Lockers						
	Install Finish Hardware		13-Mar-06	22-Mar-06	-												Iristall Finis		_				
		15			ļ				}			ļ	}	·}	· į		Brick Pa	Jorg @ T					
	Brick Pavers @ Trellis		13-Mar-06 23-Mar-06	31-Mar-06 27-Mar-06	-												Fire Alarm		: eińs				
	Fire Alarm Testing				-														or Additio _{on}				
	Obtain C of O for Addition		28-Mar-06	06-Apr-06	-								:				· A Addis:	oh Compl	or;Additio				
	Addition Complete		07-Apr-06	40.1400													◆ Additi						
	Install Owner Furnished Equipment Owner Move Into Addition		10-May-06 17-May-06	16-May-06 15-Jun-06	ļ	ļ				.		I	ļ		.				nstall Owr _{iner}	Furnished wher Move	Equipment		
