

# APPENDIX B


## PROJECT Summary / DETAILED SCHEDULE

Columbia Heights Community Center  
Summary Schedule

ID	Task Name	Duration	Start	Finish	2005												2006															
					Apr	a	Jun	Jul	Aug	e	Oct	o	De	Jan	e	Mar	Apr	a	Jun	Jul	Aug	e	Oct	o	De	Jan	e	Mar	Apr	a	Jun	Jul
1	<b>Total Project</b>	<b>546 days</b>	<b>Mon 5/3/04</b>	<b>Mon 6/26/06</b>																												
29	Design	243 days	Mon 5/3/04	Fri 4/15/05																												
30	Procurement by GC	98 days	Mon 4/18/05	Fri 9/2/05																												
31	Limited Notice to Proceed	0 days	Thu 6/30/05	Thu 6/30/05																												
2	Mobilization	5 days	Thu 6/30/05	Thu 7/7/05																												
3	Excavation	10 days	Fri 7/8/05	Thu 7/21/05																												
4	Structural Fill	15 days	Fri 7/22/05	Thu 8/11/05																												
5	Foundations	25 days	Thu 8/11/05	Thu 9/15/05																												
9	Site Utilities	28 days	Mon 9/12/05	Wed 10/19/05																												
6	Slab on Grade - Prep	2 days	Fri 9/16/05	Mon 9/19/05																												
32	Full Notice to Proceed	0 days	Mon 9/19/05	Mon 9/19/05																												
7	Erect Steel	53 days	Wed 9/21/05	Tue 12/6/05																												
8	Slab on Grade - Pour	3 days	Tue 12/6/05	Thu 12/8/05																												
11	Interior CMU and Stairs	40 days	Tue 11/15/05	Fri 1/13/06																												
12	Spray Fireproofing	18 days	Tue 11/15/05	Mon 12/12/05																												
10	Prep/Pour Slab on Decks	8 days	Thu 12/8/05	Mon 12/19/05																												
25	MEP Install & Startup	105 days	Mon 11/21/05	Thu 4/20/06																												
13	Curtain Wall	45 days	Wed 12/7/05	Thu 2/9/06																												
14	Exterior Masonry	40 days	Wed 12/21/05	Thu 2/16/06																												
15	Install Windows	20 days	Fri 2/3/06	Thu 3/2/06																												
16	Roofing System and Coping	27 days	Wed 2/8/06	Thu 3/16/06																												
18	Finishes - 1st Floor	57 days	Tue 2/14/06	Wed 5/3/06																												
19	Finishes - 2nd Floor	59 days	Tue 2/21/06	Fri 5/12/06																												
20	Finishes - 3rd Floor	60 days	Tue 2/28/06	Mon 5/22/06																												
21	Finishes - 4th Floor	59 days	Tue 3/7/06	Fri 5/26/06																												
17	Building Enclosed	0 days	Thu 3/9/06	Thu 3/9/06																												
24	Elevators Install & Testing	51 days	Thu 3/16/06	Thu 5/25/06																												
22	Gymnasium / Stage	46 days	Fri 3/24/06	Fri 5/26/06																												
23	Substantial Completion	0 days	Fri 5/26/06	Fri 5/26/06																												
27	Commisioning	19 days	Fri 5/26/06	Thu 6/22/06																												
26	Punch Out	20 days	Tue 5/30/06	Mon 6/26/06																												
28	Final Completion	0 days	Mon 6/26/06	Mon 6/26/06																												
33	Occupant Move In	0 days	Mon 6/26/06	Mon 6/26/06																												

Project: Columbia Heights Community Date: Tue 10/25/05	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Detailed Project Schedule

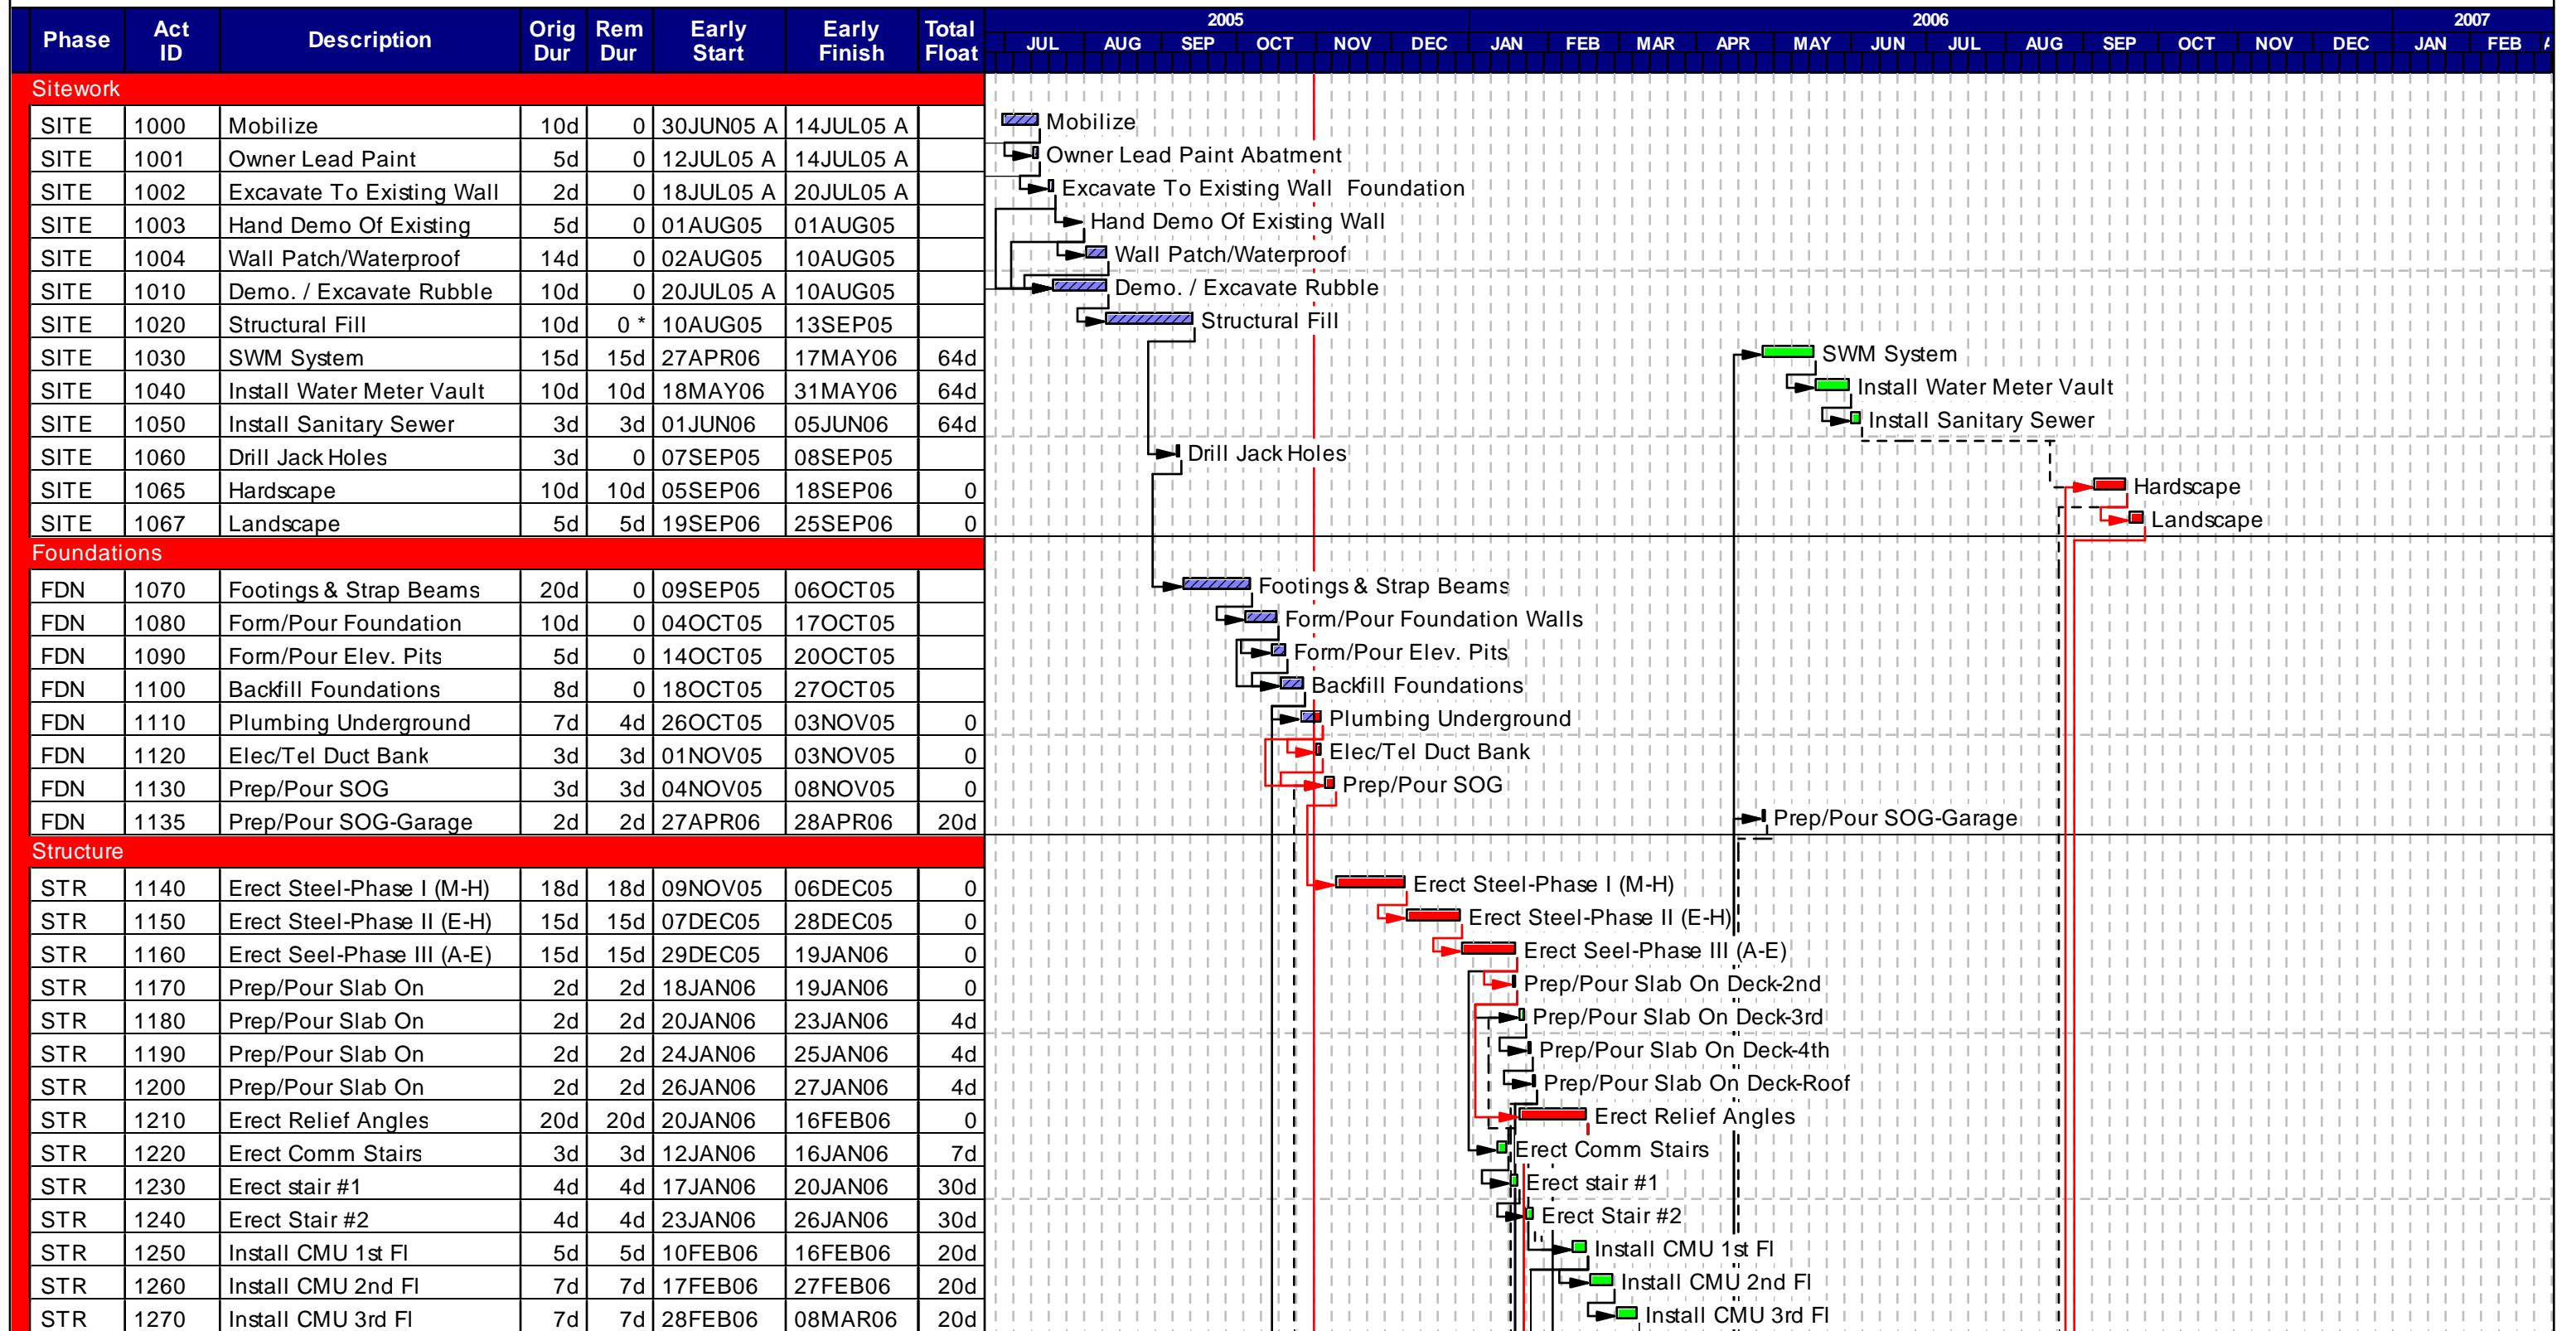


Start date	30JUN05
Finish date	16OCT06
Data date	31OCT05
Run date	31OCT05
Page number	1A
© Primavera Systems, Inc.	

Columbia Heights Community Center

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point



Detailed Project Schedule

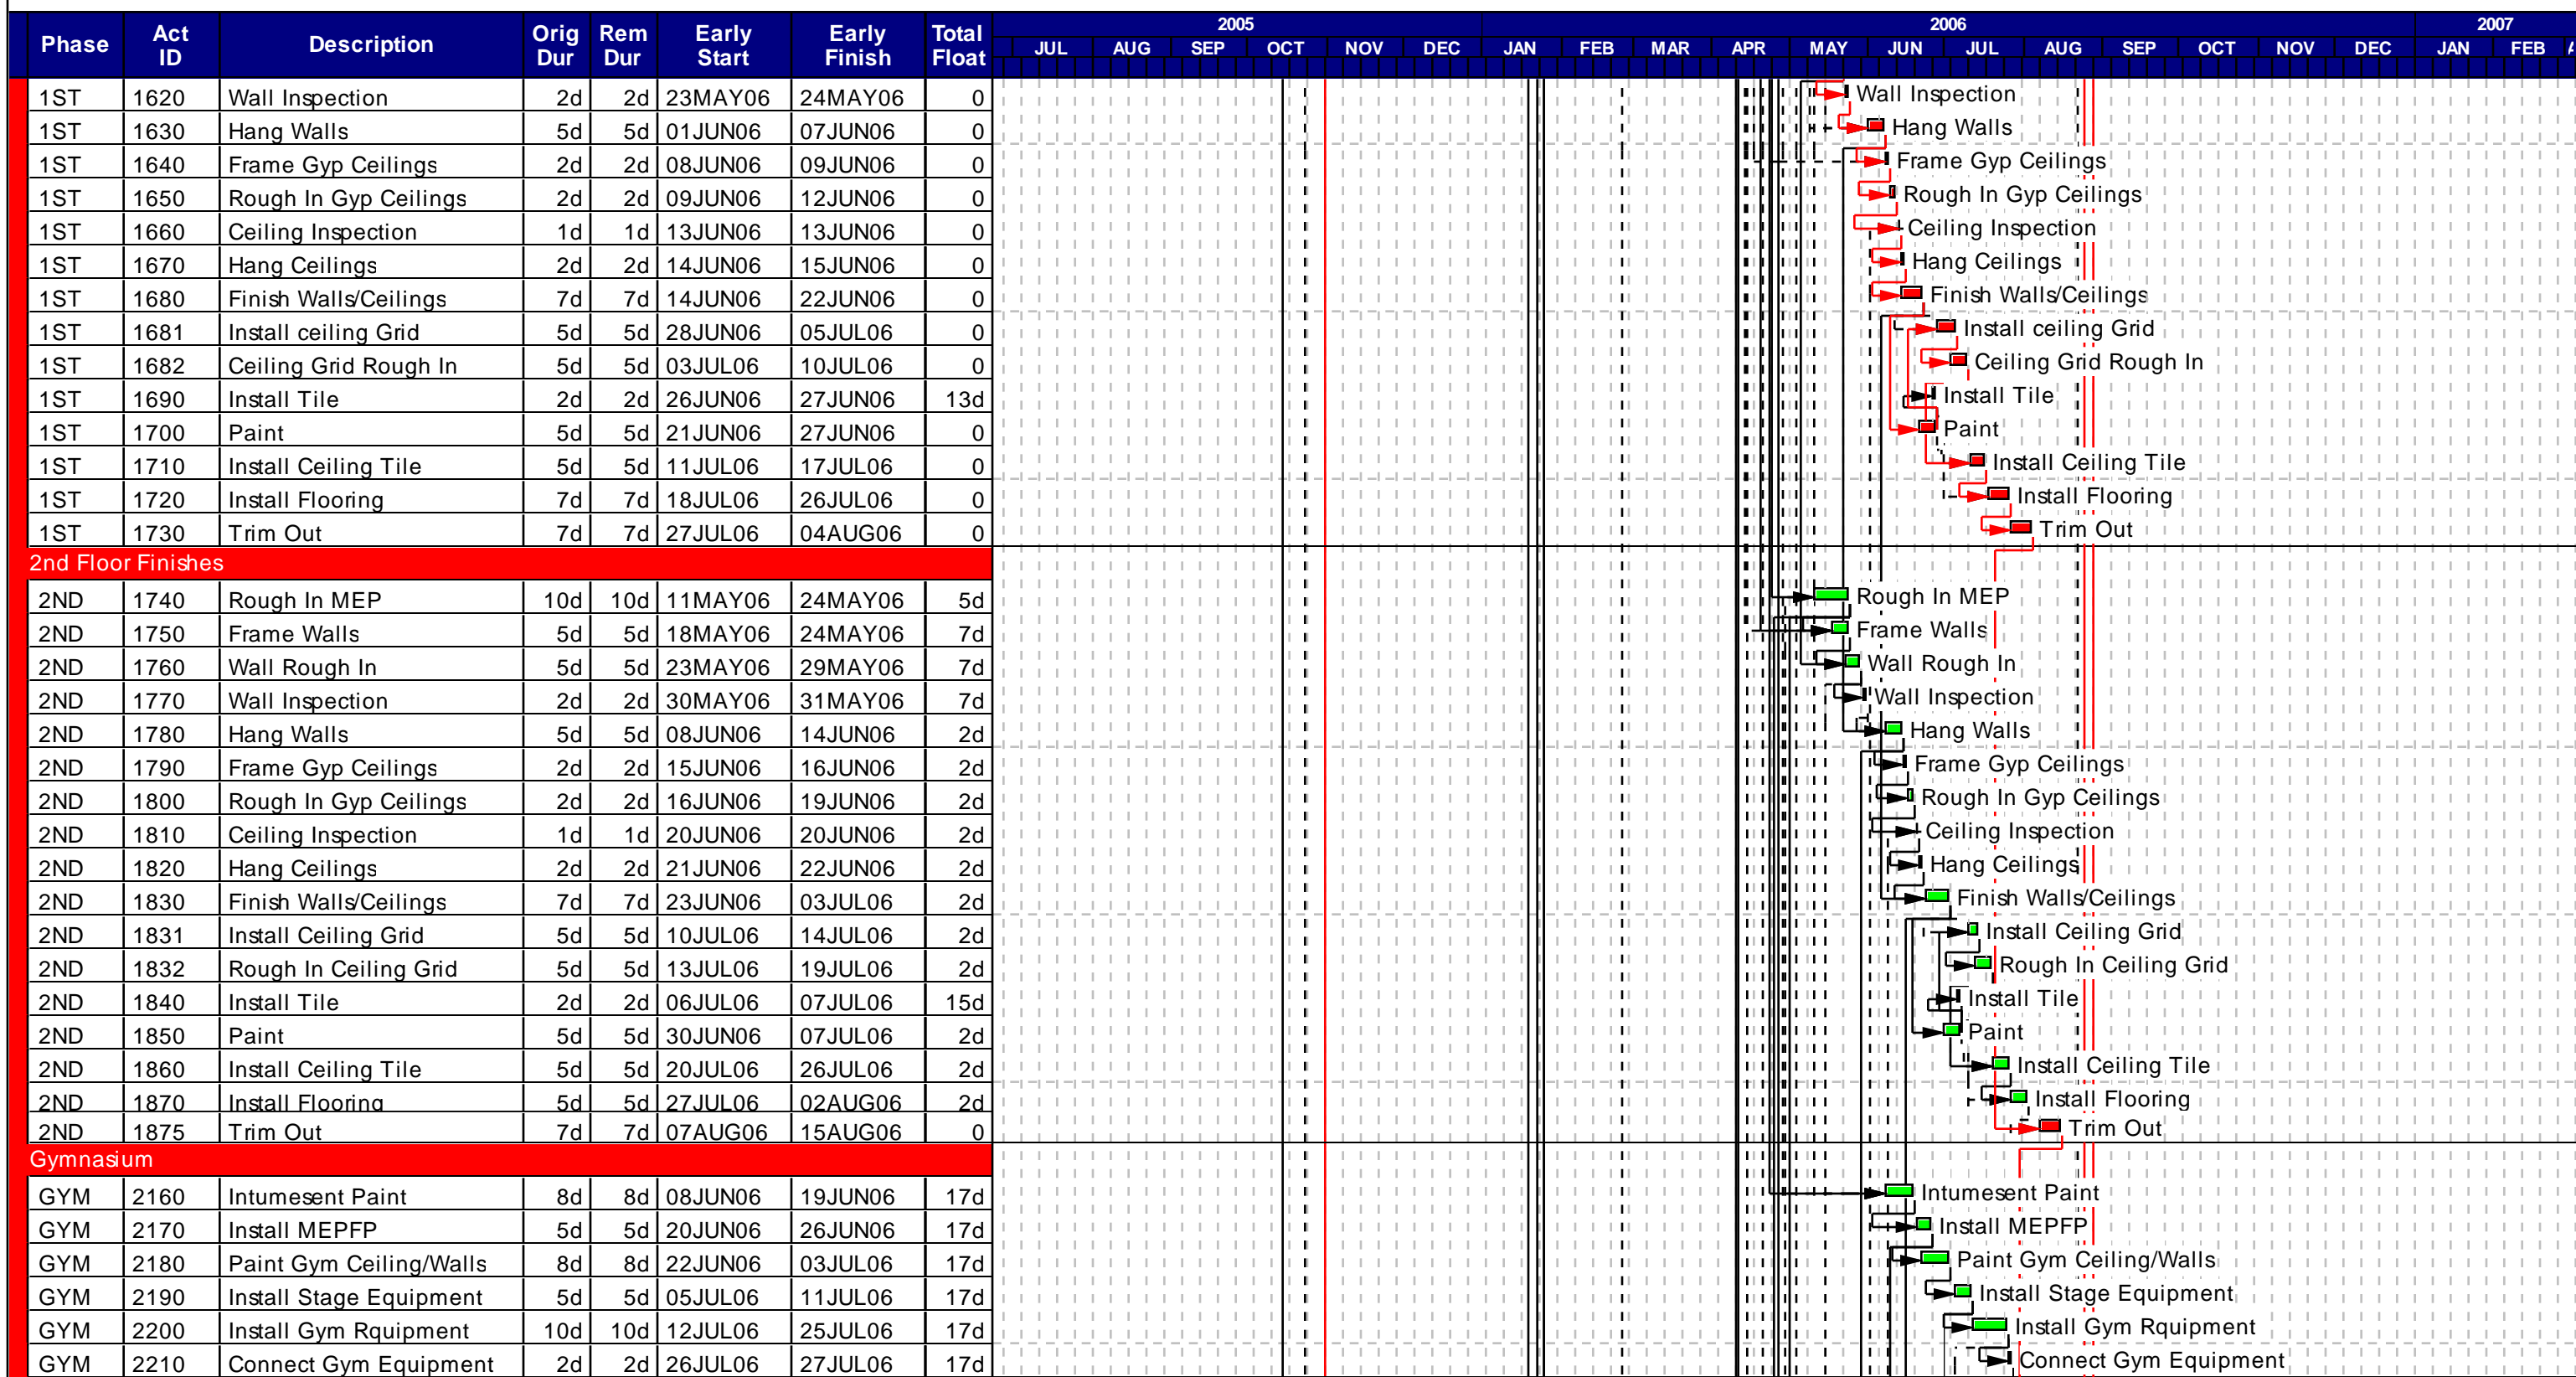

Start date 30JUN05  
 Finish date 16OCT06  
 Data date 31OCT05  
 Run date 31OCT05  
 Page number 3A  
 © Primavera Systems, Inc.

### Columbia Heights Community Center

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone poi



Detailed Project Schedule

Phase	Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2005												2006					2007		
								JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB
<b>Elevators</b>																											
ELEV	2250	Install Passanger Elevators	45d	45d	31MAY06	02AUG06	2d	Install Passanger Elevators																			
ELEV	2260	Install Service Elevator	45d	45d	13JUL06	13SEP06	2d	Install Service Elevator																			
ELEV	2270	Elevator Inspections	6d	6d	14SEP06	21SEP06	2d	Elevator Inspections																			
ELEV	2280	Elevator Generator Test	1d	1d	21SEP06	21SEP06	2d	Elevator Generator Test																			
<b>MEP</b>																											
MEP	2300	Incoming Domestic/Fire	5d	5d	03FEB06	09FEB06	43d	Incoming Domestic/Fire Service																			
MEP	2310	Duct Risers	5d	5d	30JAN06	03FEB06	68d	Duct Risers																			
MEP	2320	Storm Riser Pipe	4d	4d	10FEB06	15FEB06	43d	Storm Riser Pipe																			
MEP	2330	Sanitary Riser Pipe	3d	3d	16FEB06	20FEB06	43d	Sanitary Riser Pipe																			
MEP	2340	Domestic Riser Pipe	2d	2d	21FEB06	22FEB06	43d	Domestic Riser Pipe																			
MEP	2350	Gas Riser Pipe	2d	2d	23FEB06	24FEB06	43d	Gas Riser Pipe																			
MEP	2360	1st FI Duct	5d	5d	27APR06	03MAY06	10d	1st FI Duct																			
MEP	2370	2nd FI Duct	5d	5d	04MAY06	10MAY06	10d	2nd FI Duct																			
MEP	2380	3rd FI Duct	5d	5d	11MAY06	17MAY06	10d	3rd FI Duct																			
MEP	2390	4th FI Duct	5d	5d	18MAY06	24MAY06	10d	4th FI Duct																			
MEP	2400	Roof Duct	2d	2d	25MAY06	26MAY06	72d	Roof Duct																			
MEP	2410	Fire Pump Room	5d	5d	17FEB06	23FEB06	72d	Fire Pump Room																			
MEP	2420	Sprinkler Pipe 1st FI	5d	5d	04MAY06	10MAY06	23d	Sprinkler Pipe 1st FI																			
MEP	2430	Sprinkler Pipe 2nd FI	5d	5d	11MAY06	17MAY06	25d	Sprinkler Pipe 2nd FI																			
MEP	2440	Sprinkler Pipe 3rd FI	5d	5d	18MAY06	24MAY06	26d	Sprinkler Pipe 3rd FI																			
MEP	2450	Sprinkler Pipe 4th FI	5d	5d	25MAY06	31MAY06	26d	Sprinkler Pipe 4th FI																			
MEP	2460	Incoming Elec/Tel Duct	3d	0	26OCT05	28OCT05		Incoming Elec/Tel Duct Bank																			
MEP	2470	Set Switch Gear	5d	5d	17FEB06	23FEB06	42d	Set Switch Gear																			
MEP	2480	Feeder Conduits 1st FI	10d	10d	24FEB06	09MAR06	42d	Feeder Conduits 1st FI																			
MEP	2490	Feeder Conduits- Risers	10d	10d	07MAR06	20MAR06	42d	Feeder Conduits- Risers																			
MEP	2500	Pull Feeder Cable	10d	10d	16MAR06	29MAR06	42d	Pull Feeder Cable																			
MEP	2510	Energize Switch Gear	1d	1d	25MAY06	25MAY06	2d	Energize Switch Gear																			
MEP	2520	Energize Elevator	3d	3d	26MAY06	30MAY06	2d	Energize Elevator Disconnects																			
MEP	2530	Electric Rough In Ceilings	10d	10d	04MAY06	17MAY06	92d	Electric Rough In Ceilings & Walls 1st FI																			
MEP	2540	Electric Rough In Ceilings	10d	10d	18MAY06	31MAY06	87d	Electric Rough In Ceilings & Walls 2nd FI																			
MEP	2550	Electric Rough In Ceilings	10d	10d	25MAY06	07JUN06	87d	Electric Rough In Ceilings & Walls 3rd FI																			
MEP	2560	Electric Rough In Ceilings	10d	10d	01JUN06	14JUN06	87d	Electric Rough In Ceilings & Walls 4th FI																			
MEP	2570	Connect Roof Mech Equip.	3d	3d	29MAY06	31MAY06	72d	Connect Roof Mech Equip.																			
MEP	25800	Mech. Equipment Start Up	10d	10d	27JUN06	11JUL06	54d	Mech. Equipment Start Up																			
<b>Punchlist / Commisioning</b>																											
PNCH	2590	Punch Out	15d	15d	26SEP06	16OCT06	0	Punch Out																			
PNCH	2600	Commisioning	15d	15d	22SEP06	12OCT06	2d	Commisioning																			

Start date	30JUN05
Finish date	16OCT06
Data date	31OCT05
Run date	31OCT05
Page number	5A
© Primavera Systems, Inc.	

Columbia Heights Community Center

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point

