


The Pennsylvania State University HUB-Robeson Addition and Renovation University Park, PA

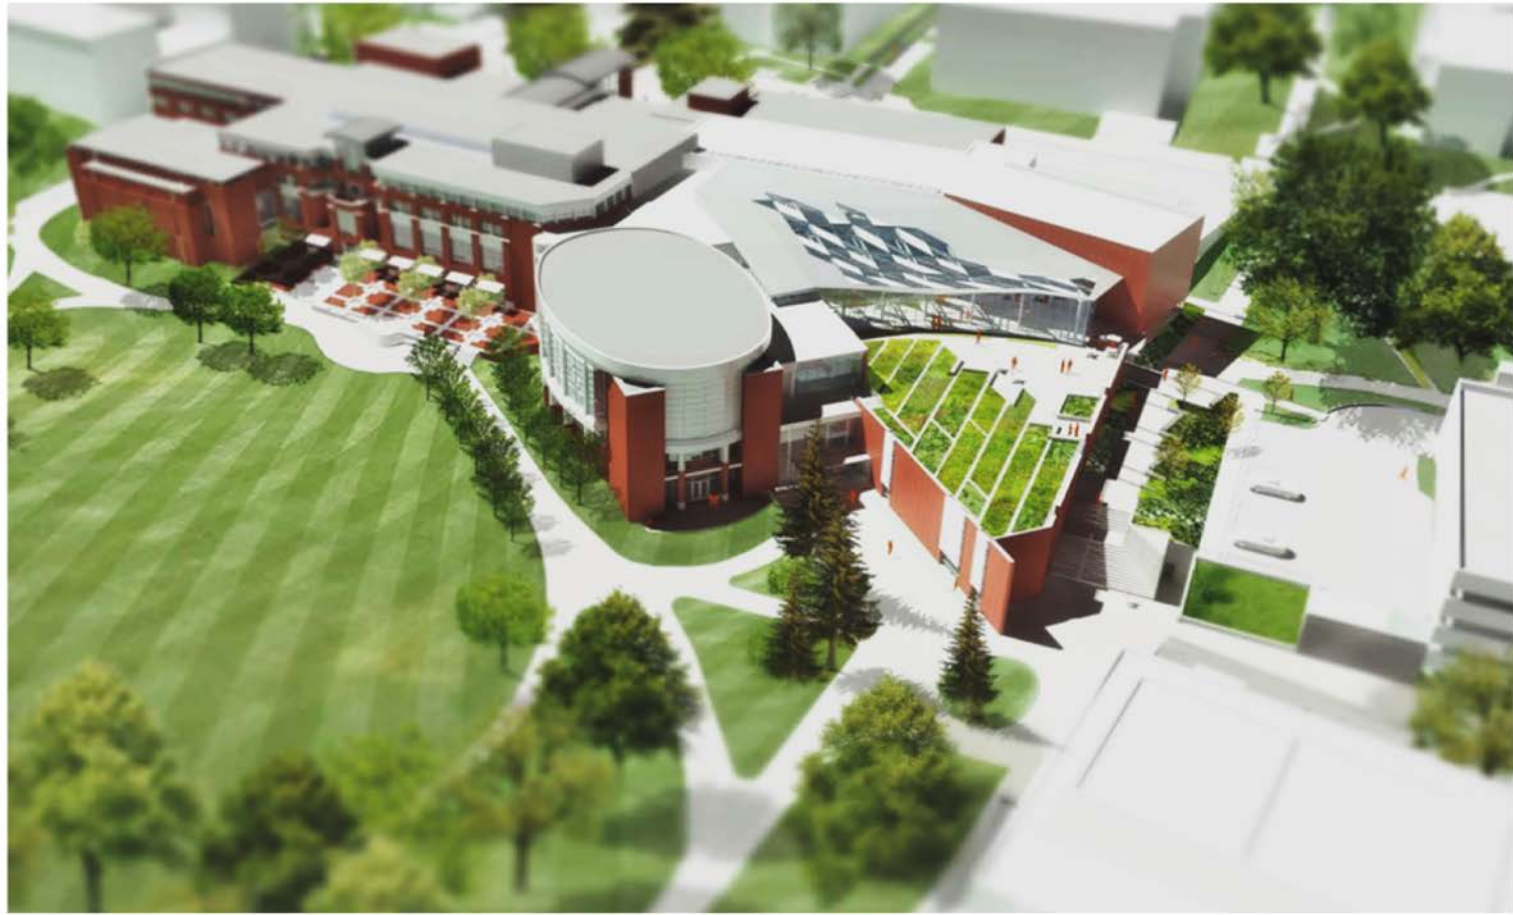

Work In Progress

- Temporary Partitions in Meeting Rooms
- Demolition of Bookstore Roof and Courtyard
- Relocation of Mechanical, Electrical, Plumbing, and Sprinkler near Ceramic Studio
- Grange Building Water Infiltration
- Excavate Coolers in Basement Crawlspace
- Core Drill in Food Service
- Exploratory Foundation work in Bookstore Basement
- Completed Tower Crane Erection

Top of Parking Deck View



HUB EXPANSION

FOR THE STUDENTS
THROUGH COMMUNITY
COLLABORATION & SAFETY



South Entrance View



Loading Dock View



Bookstore Roof Demo



Courtyard Demolition



Cooler Excavation in Basement



Tower Crane Erection



Planned Work

- Begin Drilling Piles in Courtyard
- Begin Courtyard Foundations and Grade Beams
- Begin Forming Shear Walls in Meeting Room
- Begin Temp Partition in Food Service Prep Room
- Begin Hanging Anchor Bolts near Burger King
- Continue Core Drilling in Food Service Area
- Continue Demolition of Courtyard Walls and Bookstore Roof
- Continue Demolition of Courtyard
- Continue Excavation in Courtyard
- Continue Relocation of Mechanical, Electrical, Plumbing, and Sprinkler near Ceramic Studio
- Continue Exploratory Excavation for Sub-Basement Foundations
- Continue Crawlspace Excavation
- Continue Temporary Partitions in Meeting Rooms
