




The Pennsylvania State University HUB-Robeson Addition and Renovation University Park, PA

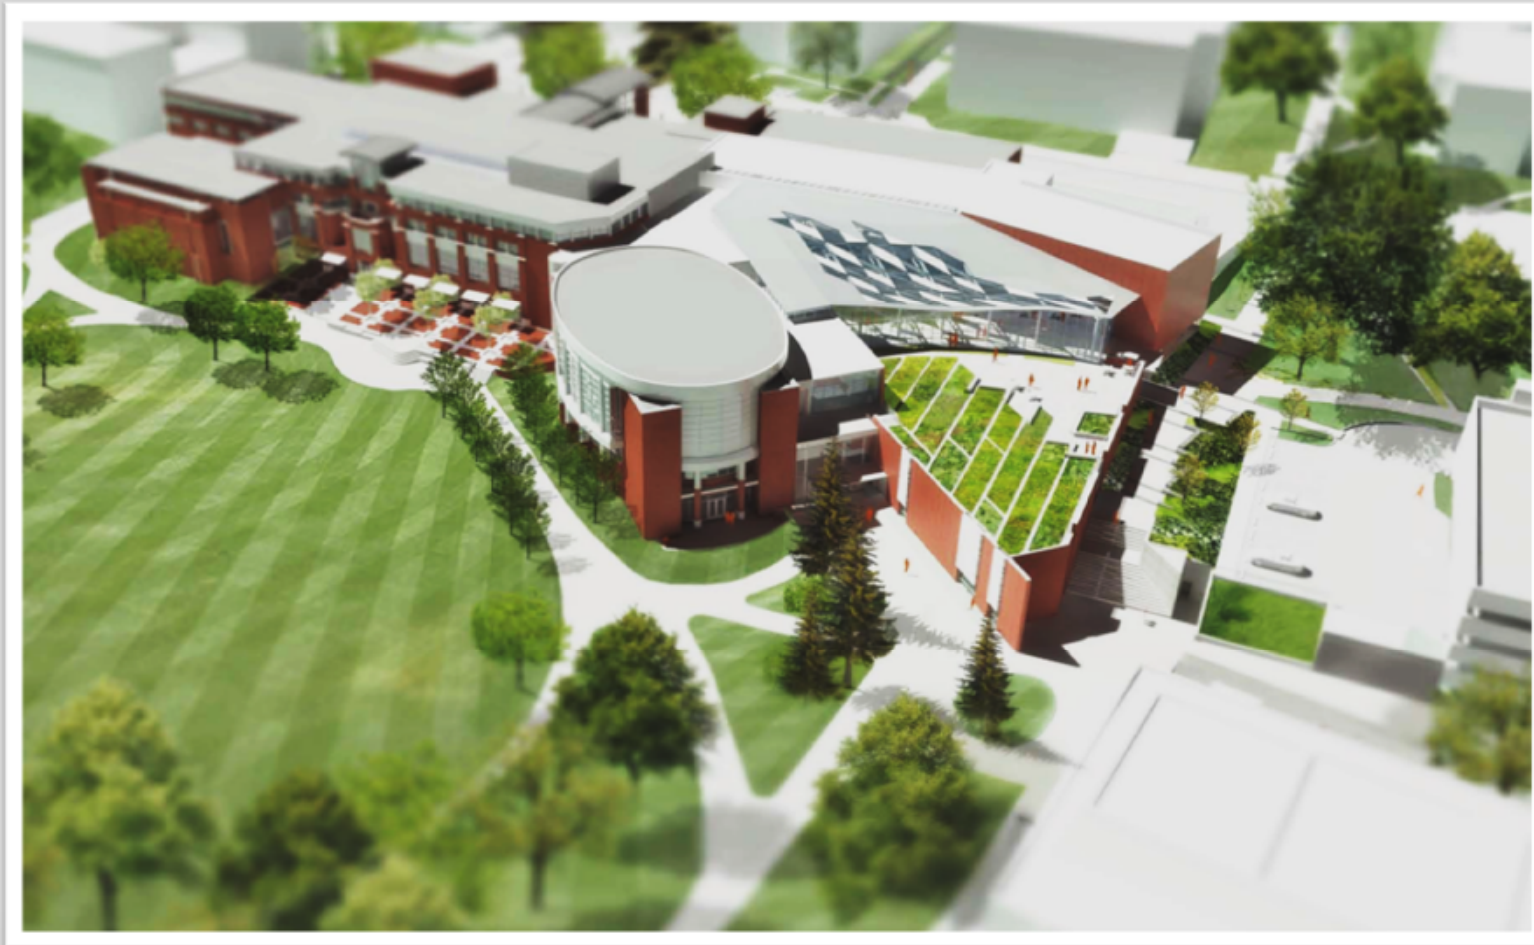

Work In Progress

- Completed Excavation for Tower Crane Foundation
- Tower Crane Foundation Leveling Slab
- Demolition of Mechanical Systems in the Bookstore
- Excavate for Pile Caps in Sub-Basement
- Demolition of Towers and Courtyard Facades
- Saw Cutting in Courtyard and Bookstore
- Ground Breaking Ceremony



HUB-Robeson Ground Breaking Ceremony





HUB-Robeson Ground Breaking Ceremony



HUB-Robeson Parking Deck View



Top of Parking Deck View



HUB
EXPANSION
FOR THE STUDENTS
THROUGH COMMUNITY
COLLABORATION & SAFETY



South Entrance View



Loading Dock View



HUB
EXPANSION
FOR THE STUDENTS
THROUGH COMMUNITY
COLLABORATION & SAFETY



© Gilbane Building Co., Inc.

Gilbane

HUB
EXPANSION
FOR THE STUDENTS
THROUGH COMMUNITY
COLLABORATION & SAFETY



© Gilbane Building Co., Inc.

Gilbane

HUB
EXPANSION
FOR THE STUDENTS
THROUGH COMMUNITY
COLLABORATION & SAFETY



Planned Work

- Form and Tie Rebar for Tower Crane
- Continue Demolition of Towers and Courtyard
- Finish Mechanical Demolition in the Bookstore
- Continue Excavation for Pile Caps in Sub-Basement
- Laser Scan Courtyard and Bookstore
- Connect New Bookstore Water Line
- Emergency Power Switchover
- Continue Grange Building Sitework (pending approval of ramp and grading changes)
