Activity ID	Activity Description	Early Start	Early Finish	Orig Dur
Milestone Activities				
1000	Notice to Proceed	12APR04		0
1010	Phase Erosion Control Complete		10JUN04	0
1020	Permanent Power Available		29JUL05	0
1030	Skylight Complete		26OCT05	0
1040	Exhibit Area Available for Exhibit		04NOV05	0
1050	Complete Landscaping		09JAN06	0
1060	Central Gallery Available for		03FEB06	0
1070	Commissioning Complete		28FEB06	0
1080	Project Complete		12APR06	0
Sitework				
1090	Professional Site Survey	12APR04	27APR04	12
1120	Install Phase 1	12APR04	08JUN04	42
1110	Install Construction Fence	06MAY04	13MAY04	6
1130	Install Temporary Construction	06MAY04	02AUG04	63
1100	Clear & Grub	10JUN04	24JUN04	11
1140	Construct Access Roads	10JUN04	29JUN04	14
Excavation				
1150	Building Bulk Excavation	21JUN04	09JUL04	15
1160	Stockpile Material	24JUN04	09JUL04	12
Utilities				
2420	Storm Drainage Culvert	14MAY04	06SEP04	82
2390	Telephone Ductbank Installation	18JUN04	04OCT04	77
2400	Sanitary Sewer Installation - Part	18JUN04	27JUL04	28
2430	Water Main Installation	09AUG04	07SEP04	22
2410	Sanitary Sewer Installation - Part	23MAY05	02JUN05	9
Foundations				
1170	Excavate/Reinforce/Place R18	12JUL04	19JUL04	6
1190	Exc/Rein/Place Inner Ring Shear	13JUL04	20JUL04	6
1180	Reinforce/Place R18 Footing	20JUL04	22JUL04	3
1210	Exc/Rein/Place R34 Shear Lug	20JUL04	27JUL04	6
1200	Reinforce/Place Inner Ring	21JUL04	23JUL04	3
1230	Exc/Rein/Place Inner Ring Shear	23JUL04	29JUL04	5
1240	Reinforce/Place Inner Ring	26JUL04	30JUL04	5
1220	Reinforce/Place R34 Footing	29JUL04	04AUG04	5
1250	Exc/Rein/Place Inner Ring Shear	29JUL04	05AUG04	6
1260	Reinforce/Place Inner Ring	02AUG04	10AUG04	7
1270	Exc/Rein/Place Grade Beams	06AUG04	16AUG04	7
1280	Exc/Rein/Place Step Footings	18AUG04	30AUG04	9
1290	Exc/Rein/Place Radial Wall	30AUG04	13SEP04	11
1300	Exc/Rein/Place C3 & C4 Wall	08SEP04	20SEP04	9
1310	Exc/Rein/Place Column Footings	15SEP04	29SEP04	11
Concrete				
1340	Form/Rein/Place/Strip Inner Ring	22JUL04	13SEP04	38
1320	Form/Rein/Place/Strip Concrete	04AUG04	05OCT04	45
1350	Form/Rein/Place/Strip Radial	10SEP04	12OCT04	23
1330	Excv/Rein/Place Elevator Pits	24SEP04	20OCT04	19
1430	Falsework/Form/Rein/Place/Strip	24SEP04	09DEC04	55
1360	Form/Rein/Place/Strip Radial	11OCT04	10NOV04	23
1390	Form/Rein/Place/Strip C4 Wall	11OCT04	02DEC04	39
1370	Form/Rein/Place/Strip Radial	19NOV04	17JAN05	42
1400	Form/Rein/Place/Strip Radial	01DEC04	22DEC04	16
1410	Form/Rein/Place/Strip C3 Wall	21DEC04	17JAN05	20

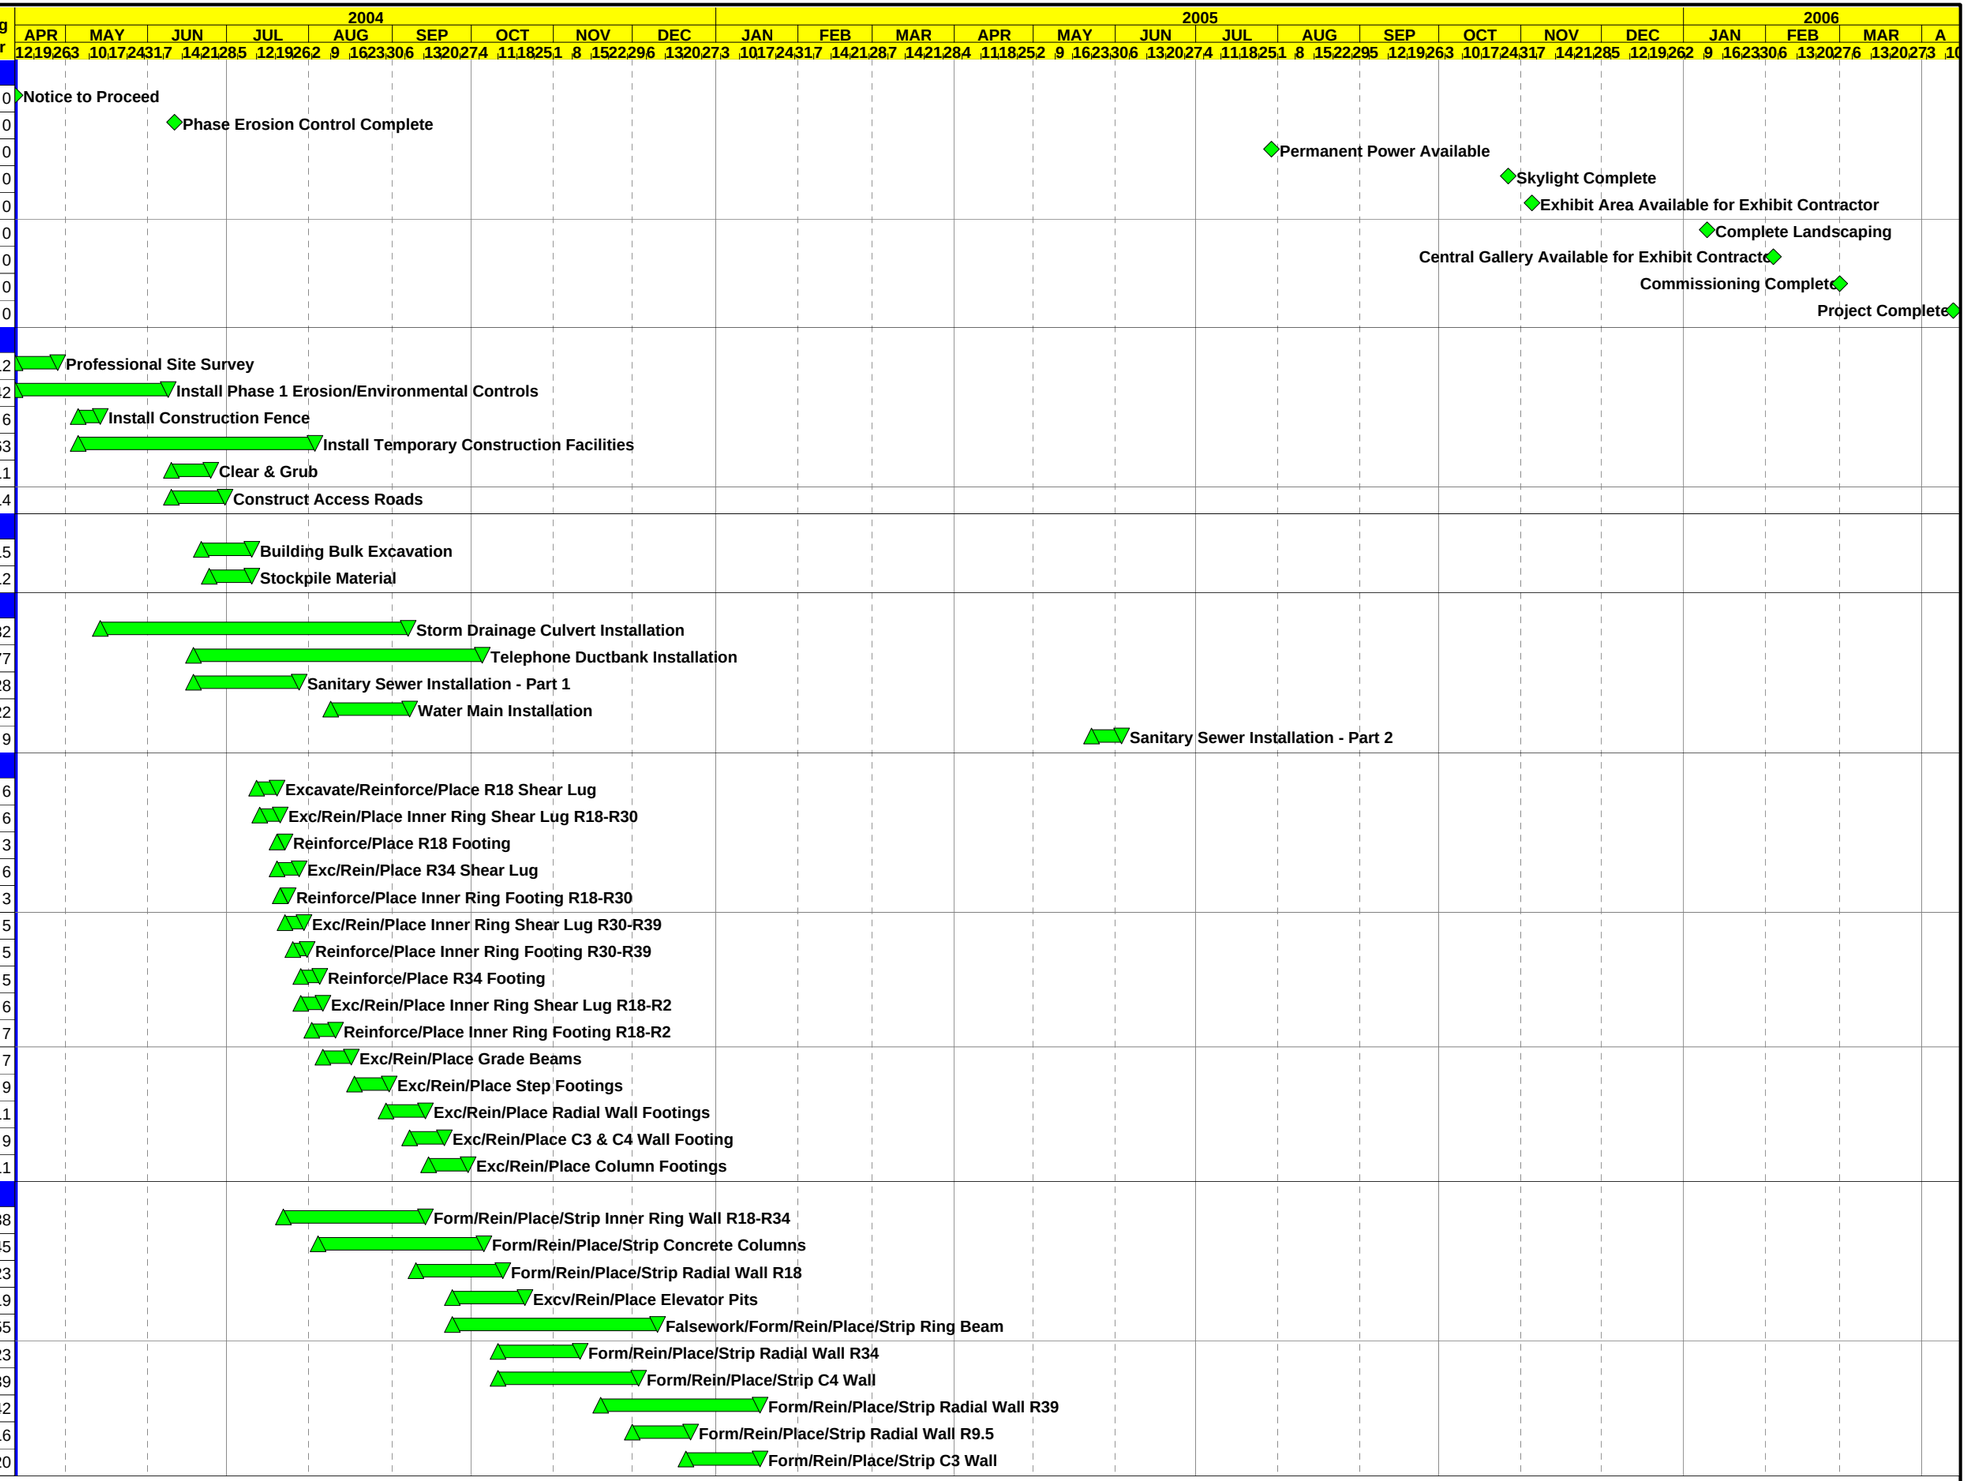

Start Date	12APR04
Finish Date	
Data Date	12APR04
Run Date	21OCT04 10:58

Early Bar
Progress Bar
Critical Activity

NMMC

Sheet 1 of 4

Michael R. Lockwood

National Museum of the Marine Corps

Classic Schedule Layout

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Early Start	Early Finish	Orig Dur
1380	Form/Rein/Place/Strip Radial	14JAN05	28FEB05	32
1420	Form/Rein/Place/Strip Exhibit	14JAN05	28FEB05	32
1460	Prep/Rein/Place/Finish SOG	21JAN05	07FEB05	12
1440	Prep/Rein/Place/Finish SOG	11MAR05	03JUN05	61
1450	Prep/Rein/Place/Finish SOG	16MAR05	01APR05	13
1470	Prep/Rein/Place/Finish SOG	25MAR05	11APR05	12
1480	Prep/Rein/Place/Finish SOG	07APR05	26APR05	14
1490	Prep/Rein/Place/Finish SOG	21APR05	06MAY05	12
Skylight Steel				
1500	Deliver / Setup Crane	16NOV04	26NOV04	9
1510	Field Assemble Mast/Erect	29NOV04	23DEC04	19
1520	Erect Ridge Beam S1, Rib Beams	27DEC04	29DEC04	3
1530	Erect Ridge Beam S5, Rib Beams	30DEC04	06JAN05	6
1540	Erect Ridge Beams S1:S5 S1:S2	07JAN05	25JAN05	13
1550	Erect Rib Beams - East Side	27JAN05	02FEB05	5
1560	Erect Rib Beams - West Side	07FEB05	03MAR05	19
1570	Erect Ridge Beams S2, S3, S4,	11FEB05	10MAR05	20
Non-Skylight Steel				
1650	Erect Balcony Steel - West Side	26NOV04	29NOV04	2
1660	Erect Observation Tower -	30NOV04	06DEC04	5
1670	Erect Balcony Steel - East Side	07DEC04	08DEC04	2
1580	Erect Steel - Mech. Roof, C1-C5,	02FEB05	08FEB05	5
1590	Erect Steel - Roof, C1-C2.1,	10FEB05	14FEB05	3
1600	Erect Steel - Roof C3-C4,	15FEB05	17FEB05	3
1610	Erect Steel - Roof C1-C3,	18FEB05	22FEB05	3
1680	Erect Stairs #2 & #3	18FEB05	28FEB05	7
1620	Erect Steel- Roof C1-C3, R8-R13,	24FEB05	28FEB05	3
1630	Erect Steel - Roof C1-C3, R3-R8	01MAR05	03MAR05	3
1640	Erect Steel - Roof C1-C3, R39-R3	04MAR05	08MAR05	3
Fireproofing				
1870	Apply Fireproofing - Outer Ring	11MAR05	05APR05	18
1880	Apply Fireproofing - Outer Ring	12APR05	20APR05	7
Masonry				
2270	Install Masonry - Exhibit Gallery	18JAN05	01FEB05	11
2260	Install Masonry - Mechanical	01MAR05	16MAR05	12
2280	Install CMU @ Theater	05MAY05	04MAY05	0
Slab-on-Metal Deck				
1690	Set Metal Deck - Balconies	30NOV04	10DEC04	9
1700	Set Metal Deck - 2nd Floor	10FEB05	14FEB05	3
1710	Set Metal Deck - Roof Areas	15FEB05	14MAR05	20
1720	Embeds/Rein/Place SOMD -	18FEB05	28FEB05	7
1730	Embeds/Rein/Place SOMD -	22FEB05	01MAR05	6
1740	Embeds/Rein/Place SOMD -	28FEB05	02MAR05	3
1750	Embeds/Rein/Place SOMD -	15MAR05	31MAR05	13
1760	Embeds/Rein/Place SOMD -	27MAY05	06JUN05	7
1770	Embeds/Rein/Place SOMD -	03JUN05	04AUG05	45
Skylight Framing and Glazing				
1780	Install Framing - S2:S3, S3:S4,	11MAR05	11APR05	22
1790	Install Glazing - S4:S5, S2:S1,	12APR05	12MAY05	23
1800	Erect Scaffolding / Install Framing	09MAY05	15JUN05	28
1810	Install Glazing - E2 to E17 /	16JUN05	15JUL05	22
1820	Erect Scaffolding / Install Framing	01JUL05	16AUG05	33
1830	Install Glazing - W2 to W17 /	18AUG05	15SEP05	21

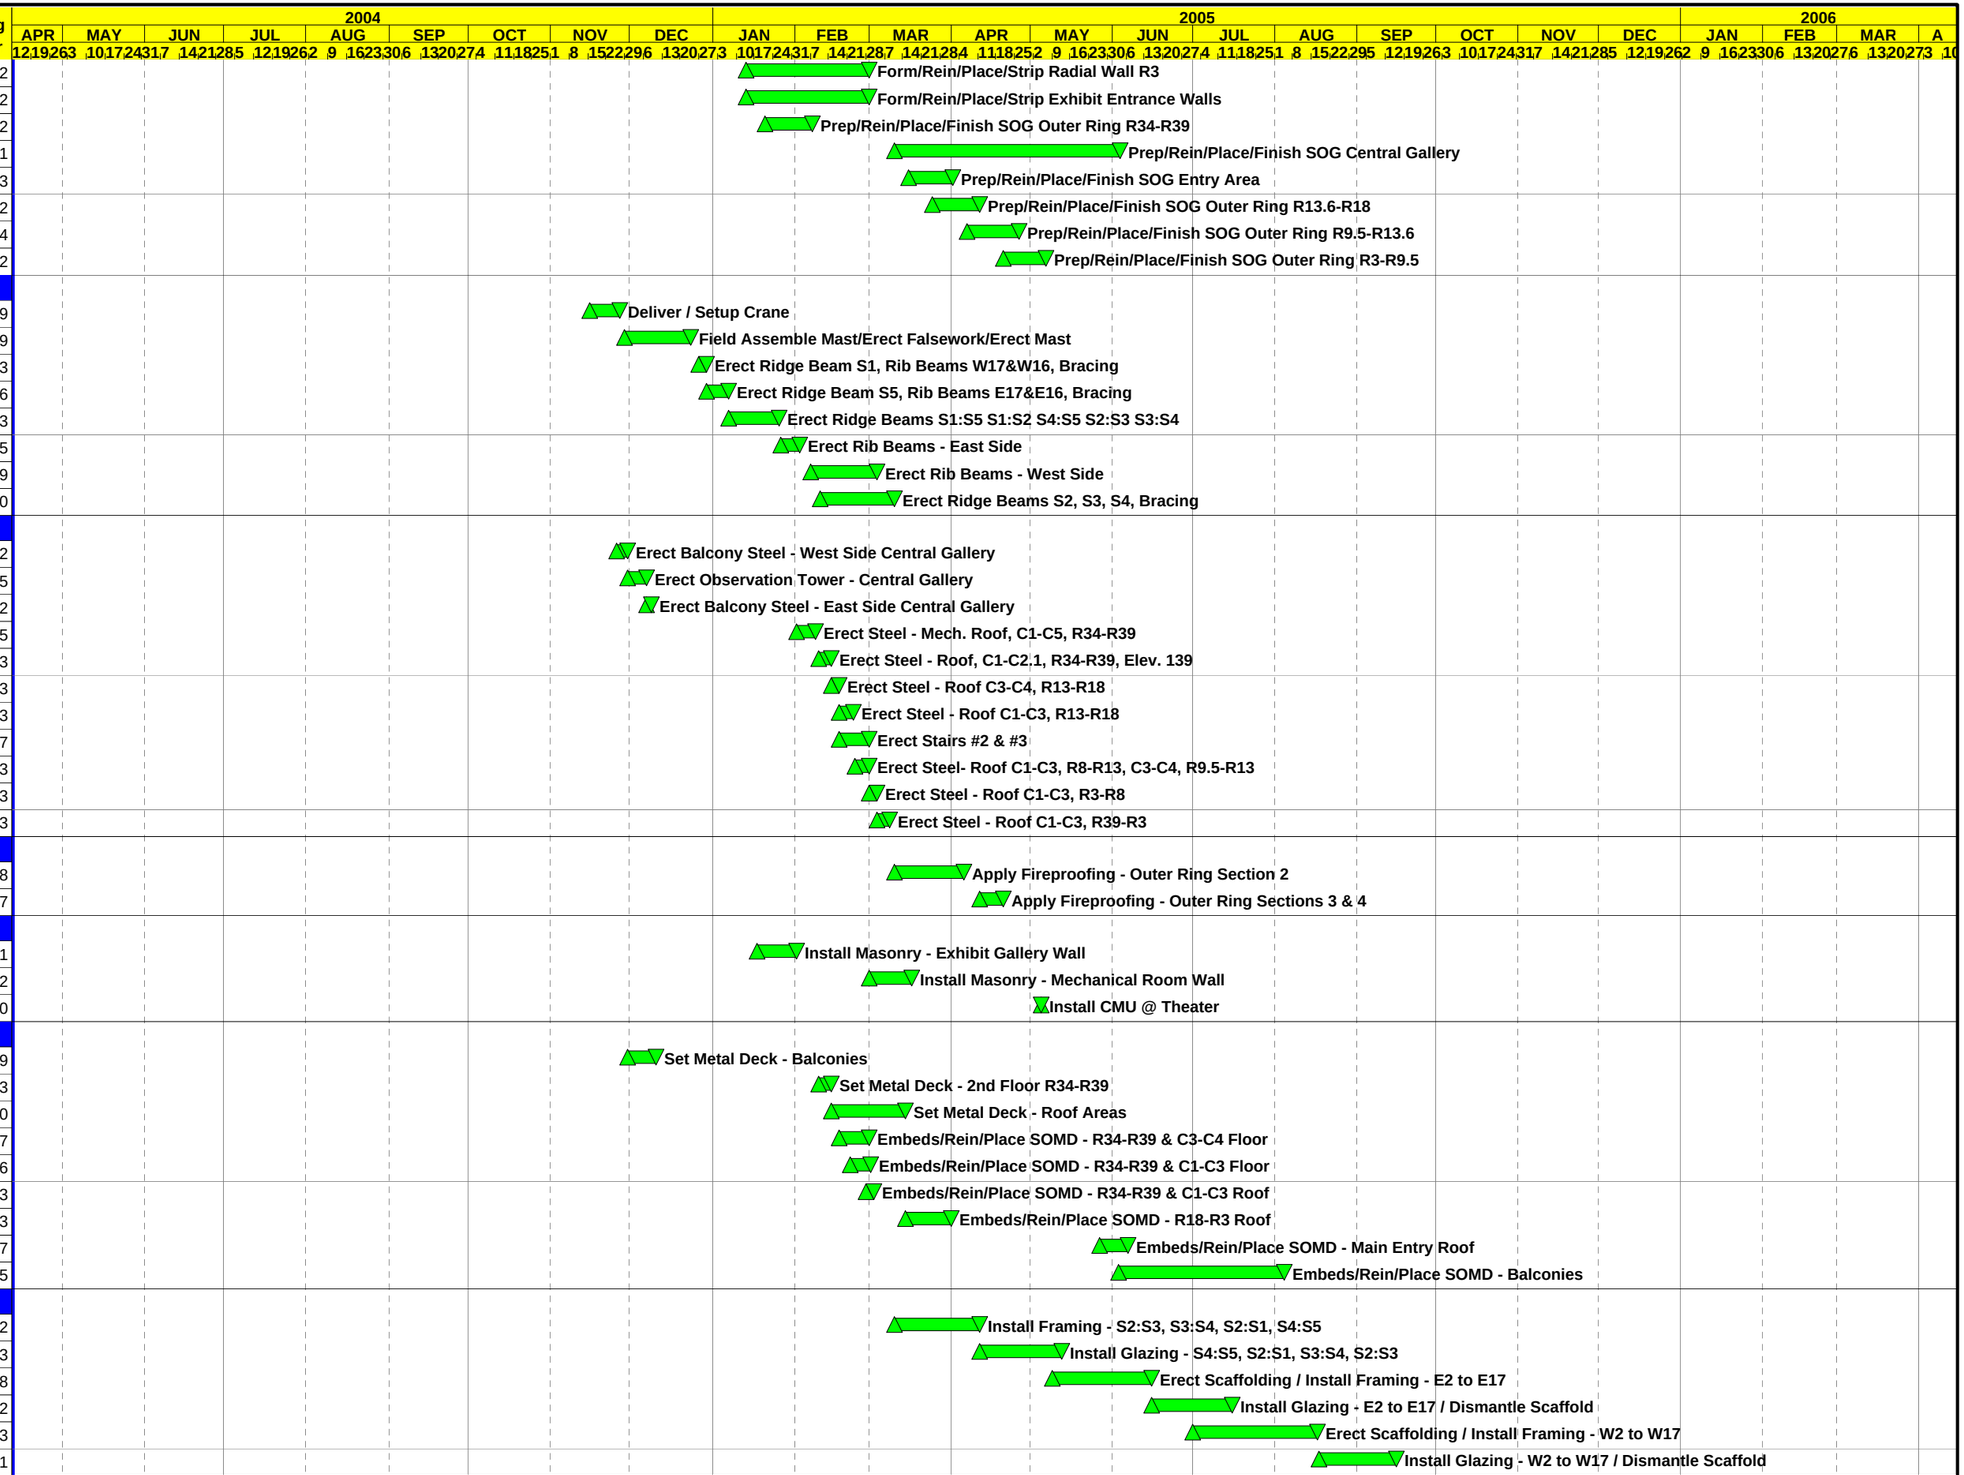

Start Date	12APR04
Finish Date	
Data Date	12APR04
Run Date	21OCT04 10:58

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

NMMC

Michael R. Lockwood

National Museum of the Marine Corps

Classic Schedule Layout

Date	Revision	Checked	Approved

Activity ID	Activity Description	Early Start	Early Finish	Orig Dur
1840	Install Framing / Glazing - North	16SEP05	29SEP05	10
Grounding and Lightning Protection				
2060	Install Grounding and Lightning	09SEP04	21OCT05	292
Mast Cladding				
1850	Install Interior Mast Cladding	18JUL05	14SEP05	43
1860	Install Exterior Mast Cladding	15SEP05	26OCT05	30
Electrical				
1910	Rough-In/Set Equipment/Pull	06APR05	29JUL05	83
1920	Rough-In Conduit / Pull Wire-	13APR05	09JUN05	42
1890	Rough-In Conduit/Pull Wire -Inner	27APR05	08JUN05	31
1900	Rough-In Electric	09MAY05	12SEP05	91
1930	Install Interior Lighting	06JUN05	11JAN06	158
1940	Install Exterior Lighting	20OCT05	16NOV05	20
Elevators				
2290	Install Elevator #1	09JUN05	21JUL05	31
2300	Install Elevator #2	21JUL05	16SEP05	42
Mechanical				
1990	Install/Insulate Sup & Ret	21SEP04	23FEB05	112
1950	Inst/Insulate Supply & Return	02NOV04	29NOV04	20
2030	Set / Install Cooling Tower 1	08FEB05	17FEB05	8
1970	Install/Insulate Supply & Return	06APR05	06JUL05	66
2010	Set / Install AHU's 1 & 2 -	06APR05	02MAY05	19
2020	Set/Install Boilers, Chillers,	06APR05	12MAY05	27
2040	Set / Install Cooling Tower 2	06APR05	13APR05	6
1960	Inst/Insulate Supply & Return	11APR05	24MAY05	32
2050	Set / Installl AHU's 3 & 4	15APR05	20MAY05	26
1980	Install / Insulate/Firestop	20APR05	21JUL05	67
2000	Install Plumbing Piping - Outer	20APR05	21JUL05	67
Sprinklers				
2310	Install Sprinkler System	11MAY05	28JUN05	35
Interior Stone Facing				
2070	Install Stone Veneer - Central	26JUL05	01NOV05	71
2080	Install Stone Veneer - Main Entry	14NOV05	22NOV05	7
Building Envelope				
2190	EPDM Sheet Roofing	03MAR05	01APR05	22
2230	Exterior Metal Wall Panel	03MAR05	09DEC05	202
2240	Option B Windows	03MAR05	13MAR06	268
2250	Green Roof	14APR05	11JUL05	63
2220	Curtain Wall	21JUN05	01SEP05	53
2200	EPDM @ Skylight Base	19JUL05	27SEP05	51
2210	Roofing @ Exhaust Fan	08SEP05	03OCT05	18
Interior Finishes				
2130	Museum Gift Shop Finishes (Incl.	06APR05	02SEP05	108
2140	1st Floor Office Area Finishes	06APR05	19SEP05	119
2160	Exhibit Gallery Finishes (Incl.	12APR05	12SEP05	110
2180	Main Entry Finishes (Incl. MEP	27APR05	11JAN06	186
2110	Toilet Room Finishes -	28APR05	06JUL05	50
2150	Theater Finishes (Incl. MEP	04MAY05	11JAN06	181
2120	2nd Floor Finishes (Incl. MEP	09MAY05	26SEP05	101
2170	Central Gallery Finishes (Incl.	17MAY05	12APR06	237
Landscaping				
2320	Place Heavy Duty Exterior Plaze	15APR05	31OCT05	142
2340	Install Irrigation Piping /	27MAY05	20SEP05	83

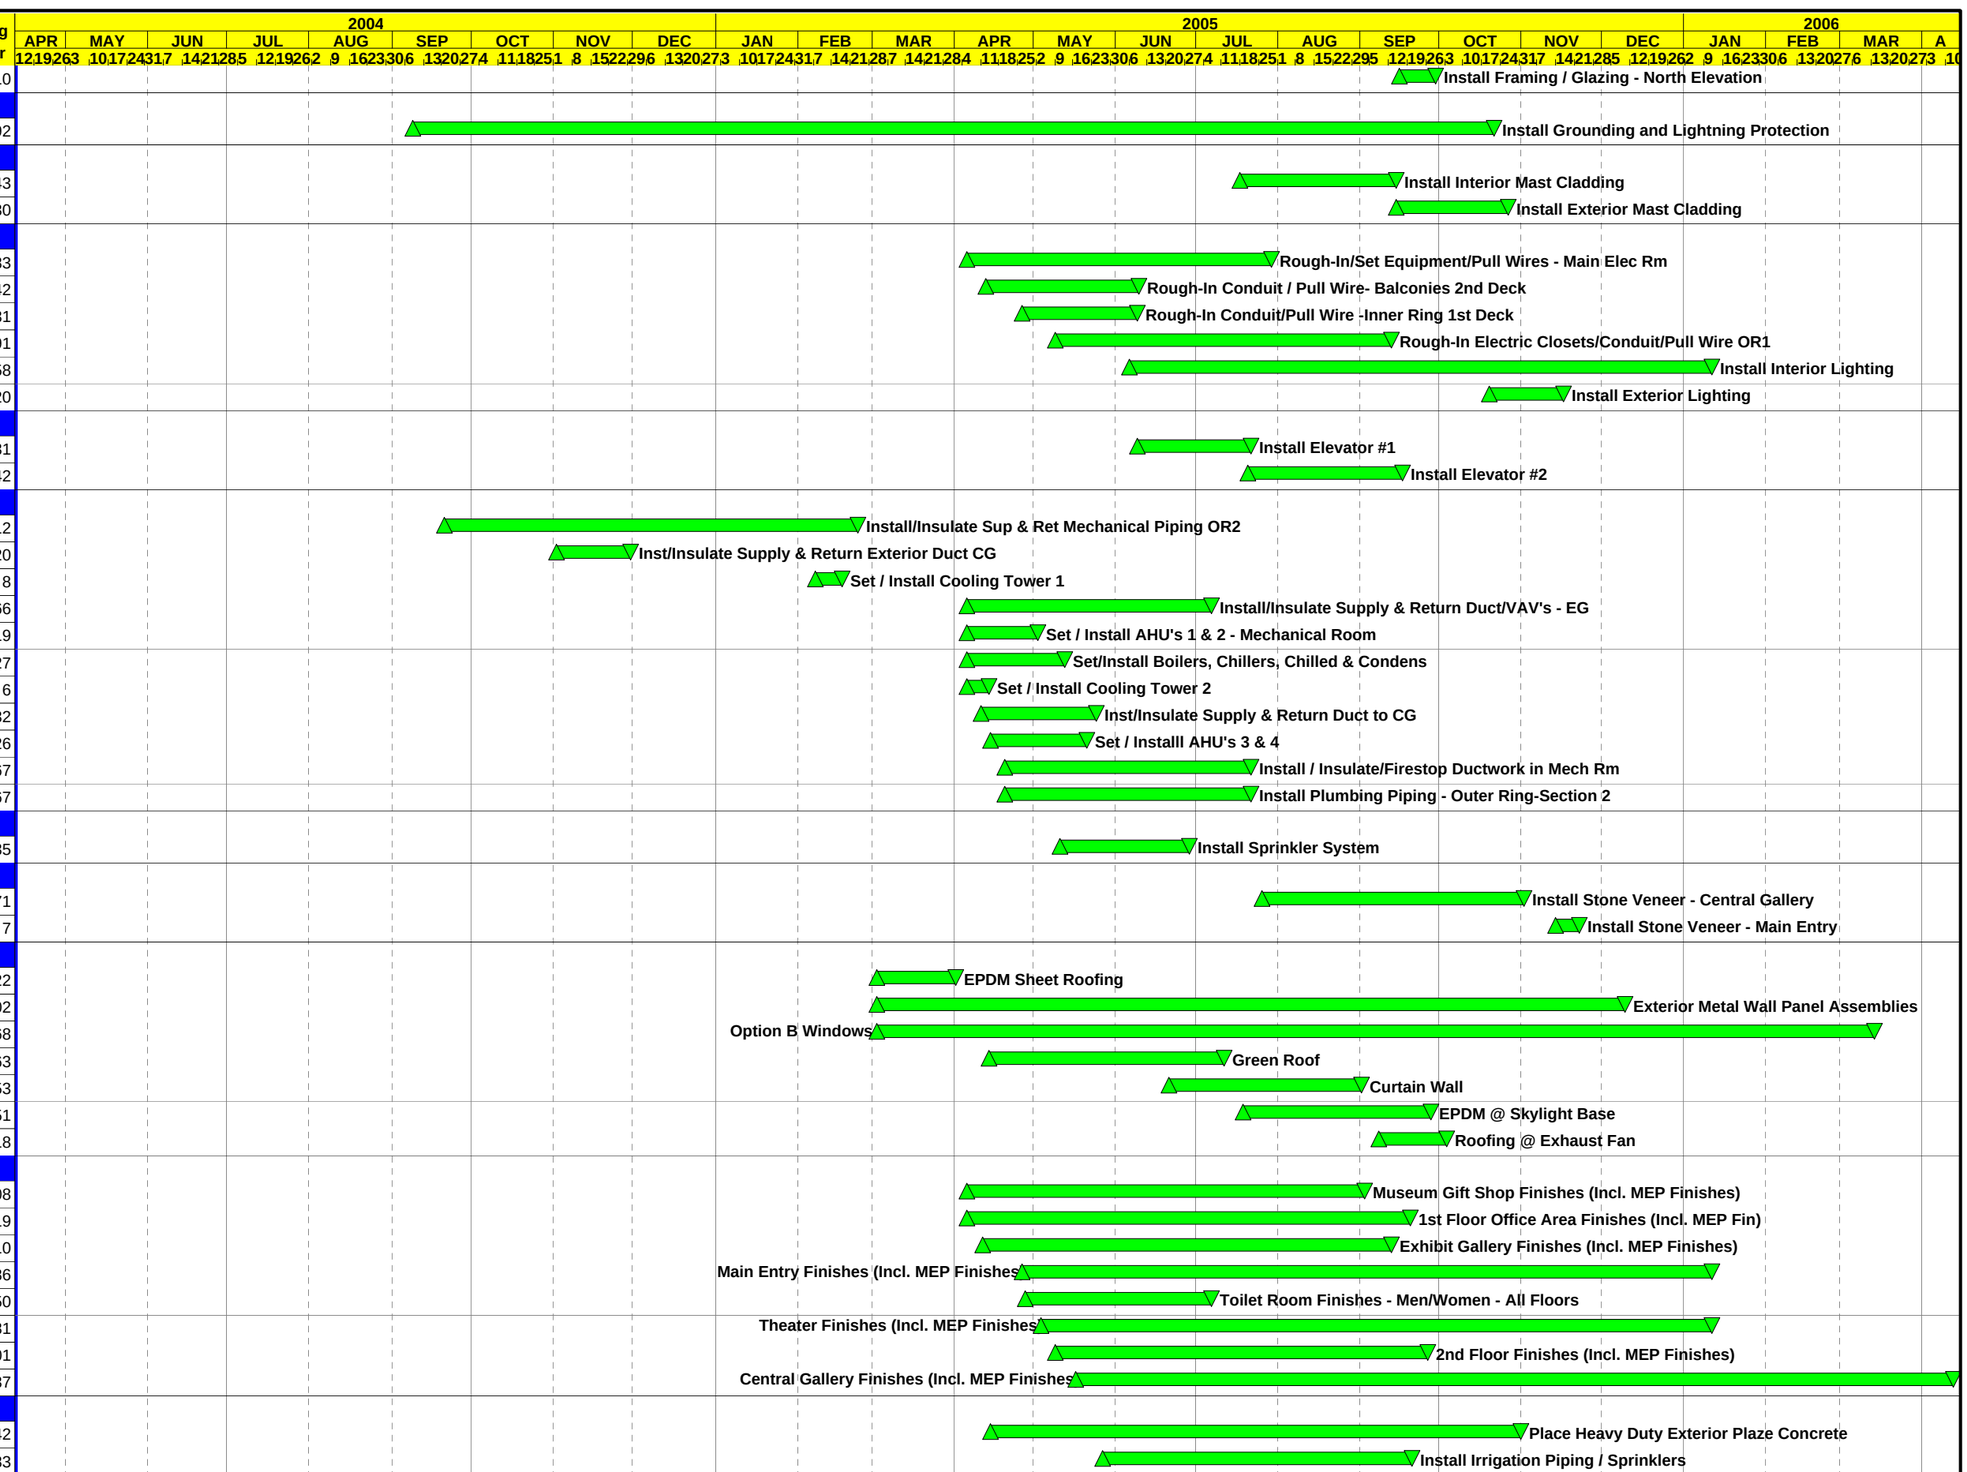

Start Date	12APR04
Finish Date	
Data Date	12APR04
Run Date	21OCT04 10:58

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

NMMC

Sheet 3 of 4

Michael R. Lockwood

National Museum of the Marine Corps

Classic Schedule Layout

Date	Revision	Checked	Approved

Activity ID	Activity Description	Early Start	Early Finish	Orig Dur
2360	Finish Retension Ponds	07JUL05	11OCT05	69
2350	Place Topsoil / Seed / Plants	21JUL05	15NOV05	84
2330	Place Asphalt Paving in Parking	26JUL05	04NOV05	74
Terrazzo Flooring				
2090	Install Terrazo - Central Gallery	19JUL05	16DEC05	109
2100	Install Terrazzo - Main Entry	26JUL05	15AUG05	15
Testing and Balancing				
2370	Testing and Balancing	30SEP05	24JAN06	83
Commissioning				
2380	Commissioning	02JAN06	28FEB06	42

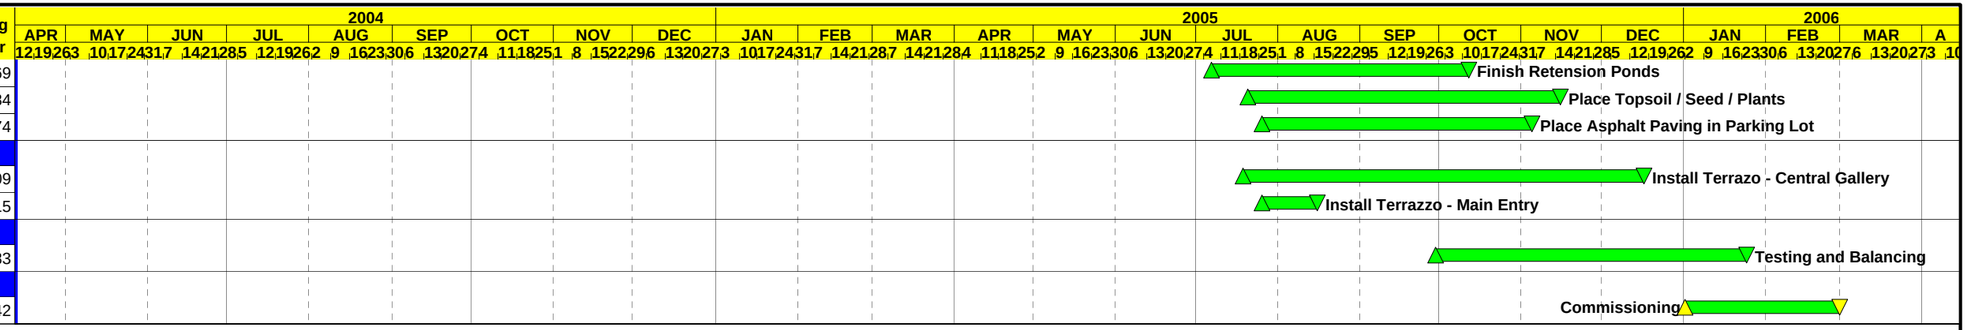

Start Date	12APR04
Finish Date	
Data Date	12APR04
Run Date	21OCT04 10:58

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

NMMC

Sheet 4 of 4

Michael R. Lockwood

National Museum of the Marine Corps

Classic Schedule Layout

Date	Revision	Checked	Approved
