
## **Penn State Rec Hall Renovation Schedule**

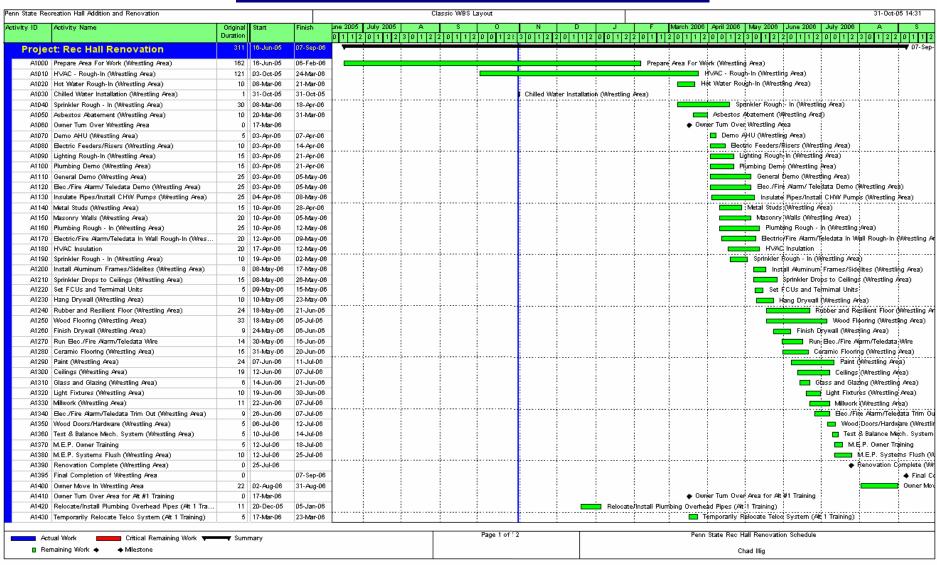

tivity ID Activity Name Original Start Finish Jon					line 2005	Classic WBryout une 2005   July 2005   A   S O   N   D   J						F March 2006 April 2006 May 2006 June 2006 July 2006 A S				
Vity 10	Activity Name	Duration	Start	rinish			1	<u> </u> 	23012	20112	0 0 1 2 2				2 2 0 1 1 2 0 0 1 2 3	
A1440	Install Feeder Conduit for Panels (At 1 Training)	8	24-Mar-06	04-Apr-06		:		:	<u> </u>						duit; for Panels (At 1 Training)	<del></del>
A1450	Construct Temporary Partitions (At 1 Training)	5	04-Apr-06	10-Apr-06									_	Construct Temp	orarly Partitions (At 1 Training)	
	Abate Area (At 1- Training)	5	04-Apr-06	10-Apr-06										Abate Area (Alt	1- Training)	
	General Demo (At 1 Training)		07-Apr-06	27-Apr-06			:							General	Demo (Alt 1 Training)	
	Masonry (At 1 Training)		11-Apr-06	24-Apr-06	†		<u> </u>	<u>.</u>					····	Wasonry		
A1490			14-Apr-06	20-Apr-06			!								emo (Alt 1 Training)	
A1500	, ,,		18-Apr-06	02-May-06	-									- :	ical Rough In (Alt 1 Training)	
	Ceramic Tile (At 1 Training)		25-Apr-06	08-May-06	1										amic Tile (Alt 1 Training)	
	Set HVAC Equip. (All of Alt 1)	5	-	04-May-06	-										IVAÇ Equip. (All of Alt 1)	
	Doors/Hardware (Att 1 Training)	5	28-Apr-06	04-May-06	·····	· <del> </del>	<del></del>	<del>.</del>							s/Hardware (Alt 1: Training)	
	Plumbing Pipe (At 1 Training)	10	28-Apr-06	11-May-06	-			1							umbing Pipe (Alt ) Training)	
	HVAC Final Connections (At 1 Training)	10	05-May-06	18-May-06	-		:								HVAC Final Connections (Att	1 Training)
	Paint (At 1 Training)	15	05-May-06	25-May-06											Paint (At 1 Training)	
			09-May-06	18-May-06	-										Set Plumbing Fixtures (At 1 )	mining)
	Set Plumbing Fixtures (At 1 Training)		-	-			ļ	<u>‡</u>						·	Run Bec./Fire Alarm/Tel	
A1580	, ,,	4		01-Jun-06	-										Accoustical Ceiling (	,
	Accoustical Ceiling (At 1 Training)		02-Jun-06	08-Jun-06												
	Bec./Fire Alarm/Teledata Trim Out (Alt 1 Training)		02-Jun-06	13-Jun-06											Bec./Fire Alarm/Te	
	GRDs Installation (At 1 Training)	4	Do Dan Do	14-Jun-06											GRDs Installation	
	Millwork (At 1 Training)		09-Jun-06	22-Jun-06	ļ		<u>.</u>	<u>:</u>							Millwork (At 1	
	Carpet/Rubber Flooring (Alt 1 Training)		21-Jun-06	27-Jun-06												r Flooring (Alt 1 Tra
	At 1 Training Complete	0		10-Jul-06											♦ Alt 1 Tra	ining Complete
	Owner Move In Training (Alt 1 Training)	9	22-Aug-06	01-Sep-06												Owne
A1660	Asbestos Abatement (Alt 1 Locker)	10	17-Mar-06	30-Mar-06			:			:		:			t (Att 1 Locker)	:
A1670	Demo HVAC (At 1 Locker)	5	31-Mar-06	06-Apr-06	1	<u> </u>	<u>.</u>						<u> </u>	emo HVAC (Alt		<u>i</u>
A1680	Demo Plumbing (At 1 Locker)	15	31-Mar-06	20-Apr-06				i							ibing (Alt 1 Locker)	i
A1690	General Demolition (At 1 Locker)	15	31-Mar-06	20-Apr-06									<u> </u>	General De	molition (Att 1 Locker)	
A1700	HVAC/Plumbing Overhead (Alt 1 Locker)	15	07-Apr-06	27-Apr-06		1								HVAC/P	lumbing Overhead (At 1 Locke	r)
A1710	Masonry (At 1 Locker)	10	14-Apr-06	27-Apr-06										Masonry (	(Alt 1 Locker)	
A1720	Duct Rough Ins (At 1 Locker)	8	28-Apr-06	09-May-06											nt Rough Ins (Alt 1 Locker)	
A1725	Bectrical Rough In (Alt 1 Locker)	10	28-Apr-06	11-May-06	1									, B	ectrical Rough In (Alt 1 Locker)	
A1730	Furr and Gyp Installation (At 1 Locker)	10	28-Apr-06	11-May-06								:		Ė Fu	ırranıd Gyp Installation (Alt 1 🕻	ocker)
A1740	Ceiling Installation ( Alt 1 Locker)	14	12-May-06	01-Jun-06										_	Ceiling Installation ( At	Locker)
A1750	Finish Drywall (At 1 Locker)	3	19-May-06	23-May-06											Finish Drywall (At 1 Locker	
A1760	Terrazzo Tile (Att 1 Locker)	3	02-Jun-06	06-Jun-06											☐ Terrazzo Tile (Alt 1 Lo	ker)
	Ceramic Tile (At 1 Locker)	8	02-Jun-06	13-Jun-06	†		:	. <del>.</del>							Ceramic Tile (At 1;	Locker)
	Paint (At 1 Locker)		07-Jun-06	16-Jun-06											Paint (Alt 1 Locke	
	GRDs (At 1 Locker)		21-Jun-06	21-Jun-06	1										I GRDs (Att 1 Lo	
	Sprinkler Heads (Alt 1 Locker)		21-Jun-06	21-Jun-06											Sprinkler Heads	
	Carpet (Alt 1 Locker)	4		27-Jun-06	1										Carpet (Alt 1	
	VCT (At 1 Locker)	9		05-Jul-06	<del> </del>	· <del> </del>	<del></del>	<del>-</del>							VCT (At	
	Plumbing Fixtures (At 1 Locker)		14-Jul-06	20-Jul-06			i									nbing Fixtures (Alt 1
	Millwork (At 1 Locker)		14-Jul-06	20-Jul-06	-										and the second s	Jork (At 1 Lácker)
	Maple Lockers (At 1 Locker)	9	14-Jul-06	26-Jul-06			:									taple Lockers (At 1
	· · · · · · · · · · · · · · · · · · ·	0	1-201-00	26-Jul-06	-											omplete At 1 Locks
	Complete Alt 1 Locker Room Final Completion of Alt 1	0		26-Jul-06 21-Aug-06	ļ		<u> </u>	<u> </u>							*!	omplete At i Locke
A1870	Final Completion of At 1	U		21-Aug-06		:	:	!	<u> </u> :	: :	:		:	:	<u> </u>	→ Final Con
Actual Work Critical Remaining Work								Page 2 of 2								
												Penn State Rec Hall Renovation Schedule				
. P.	maining Work • • Milestone													Chad Illig		
