

Project: Building Envelope Schedule
Date: Mon 4/3/06

Task Progress

Milestone Summary

Group By Summary

Deadline

External Tasks

Project Summary


Rolled Up Progress


Split

Rolled Up Task

Rolled Up Milestone

Page 1

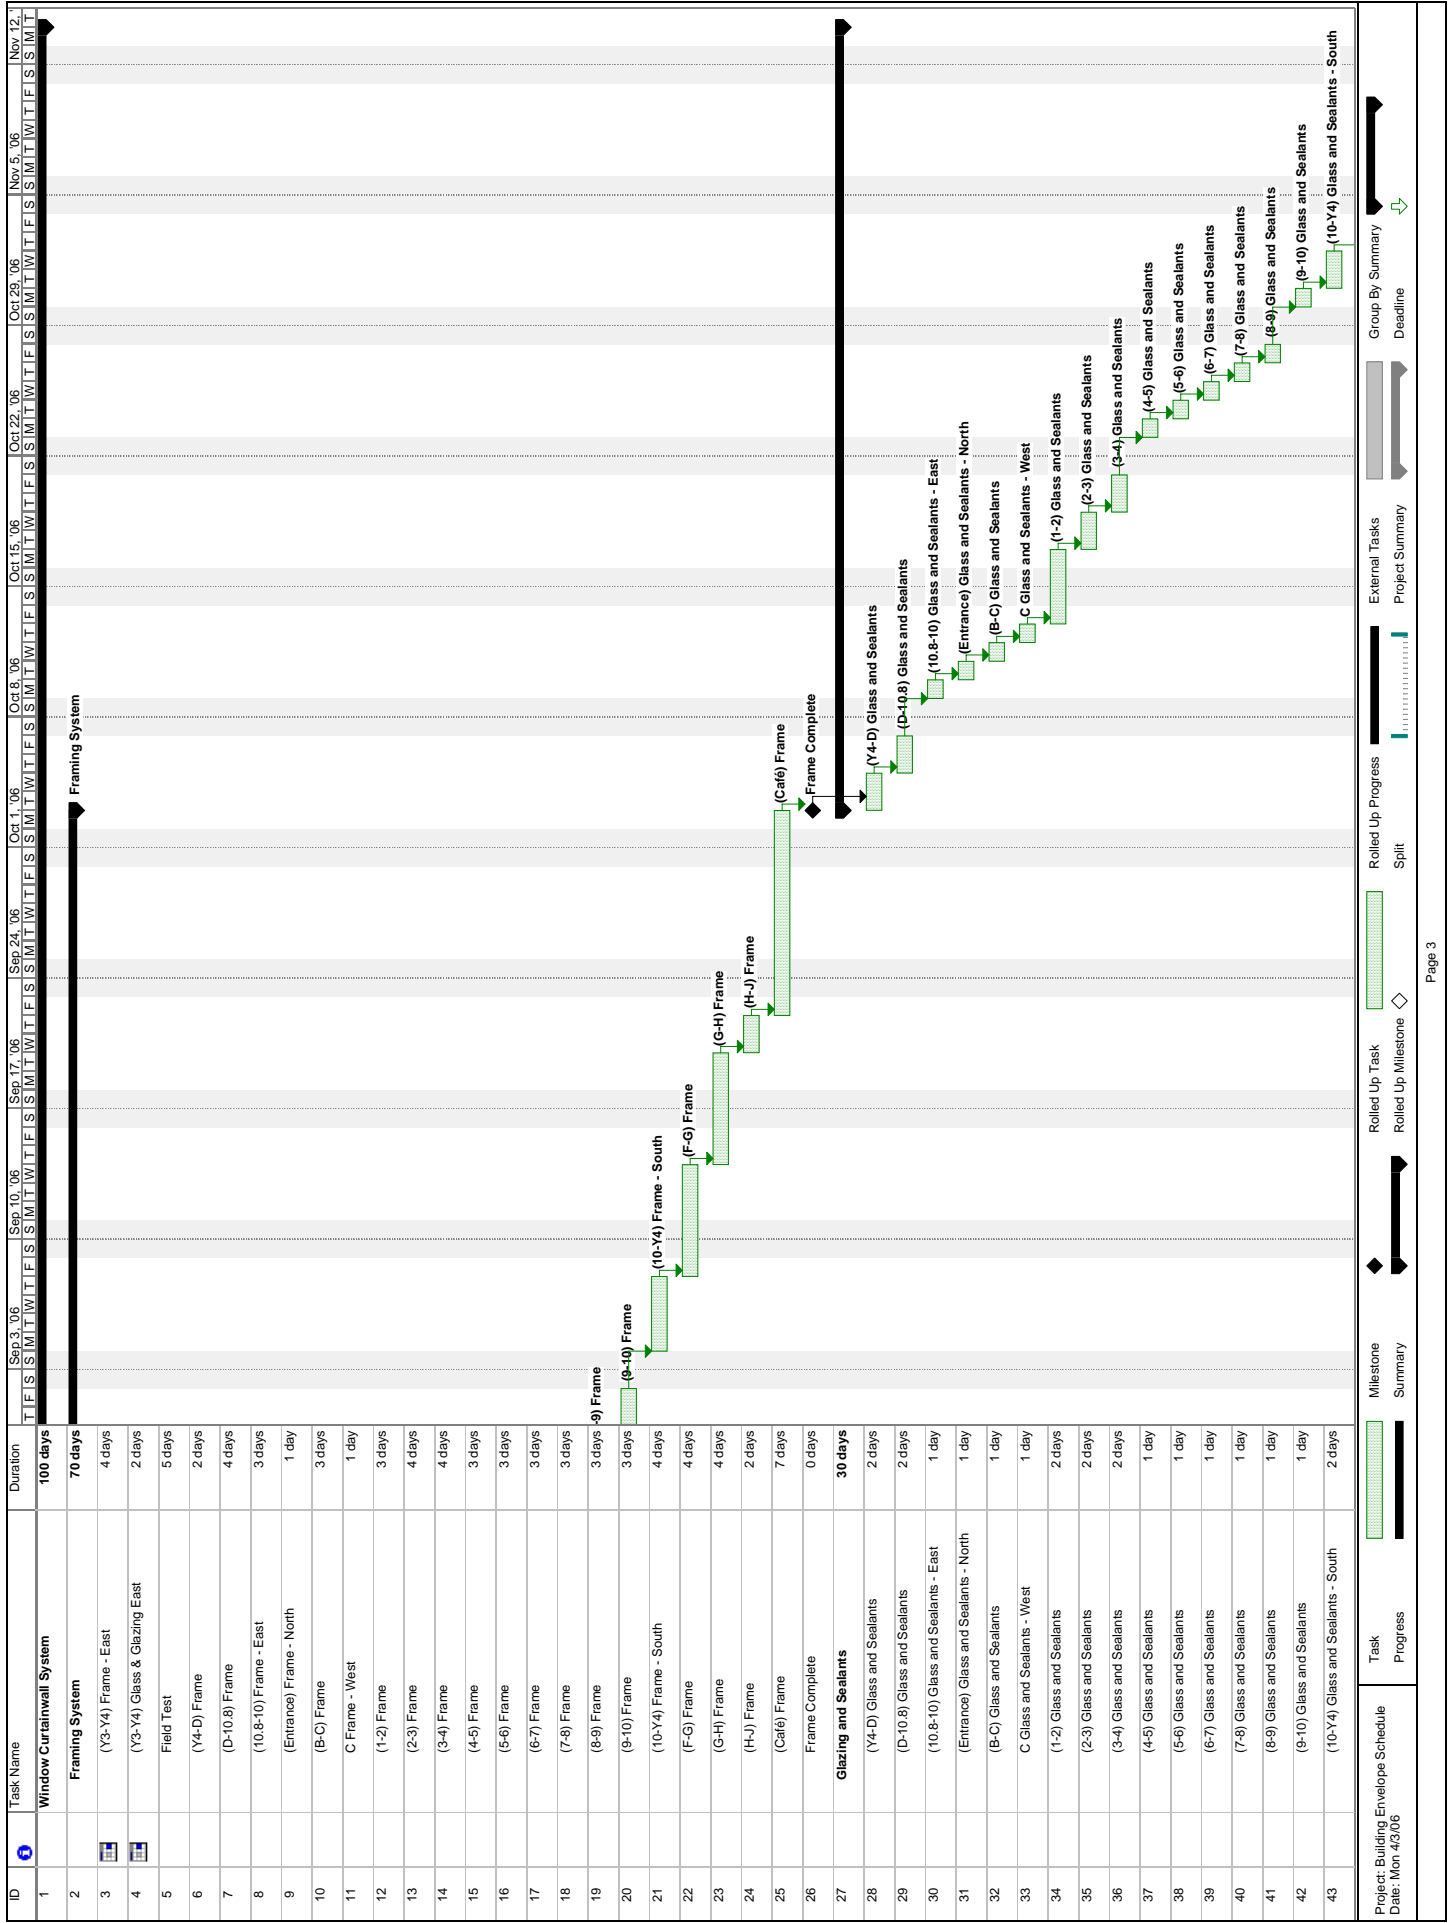

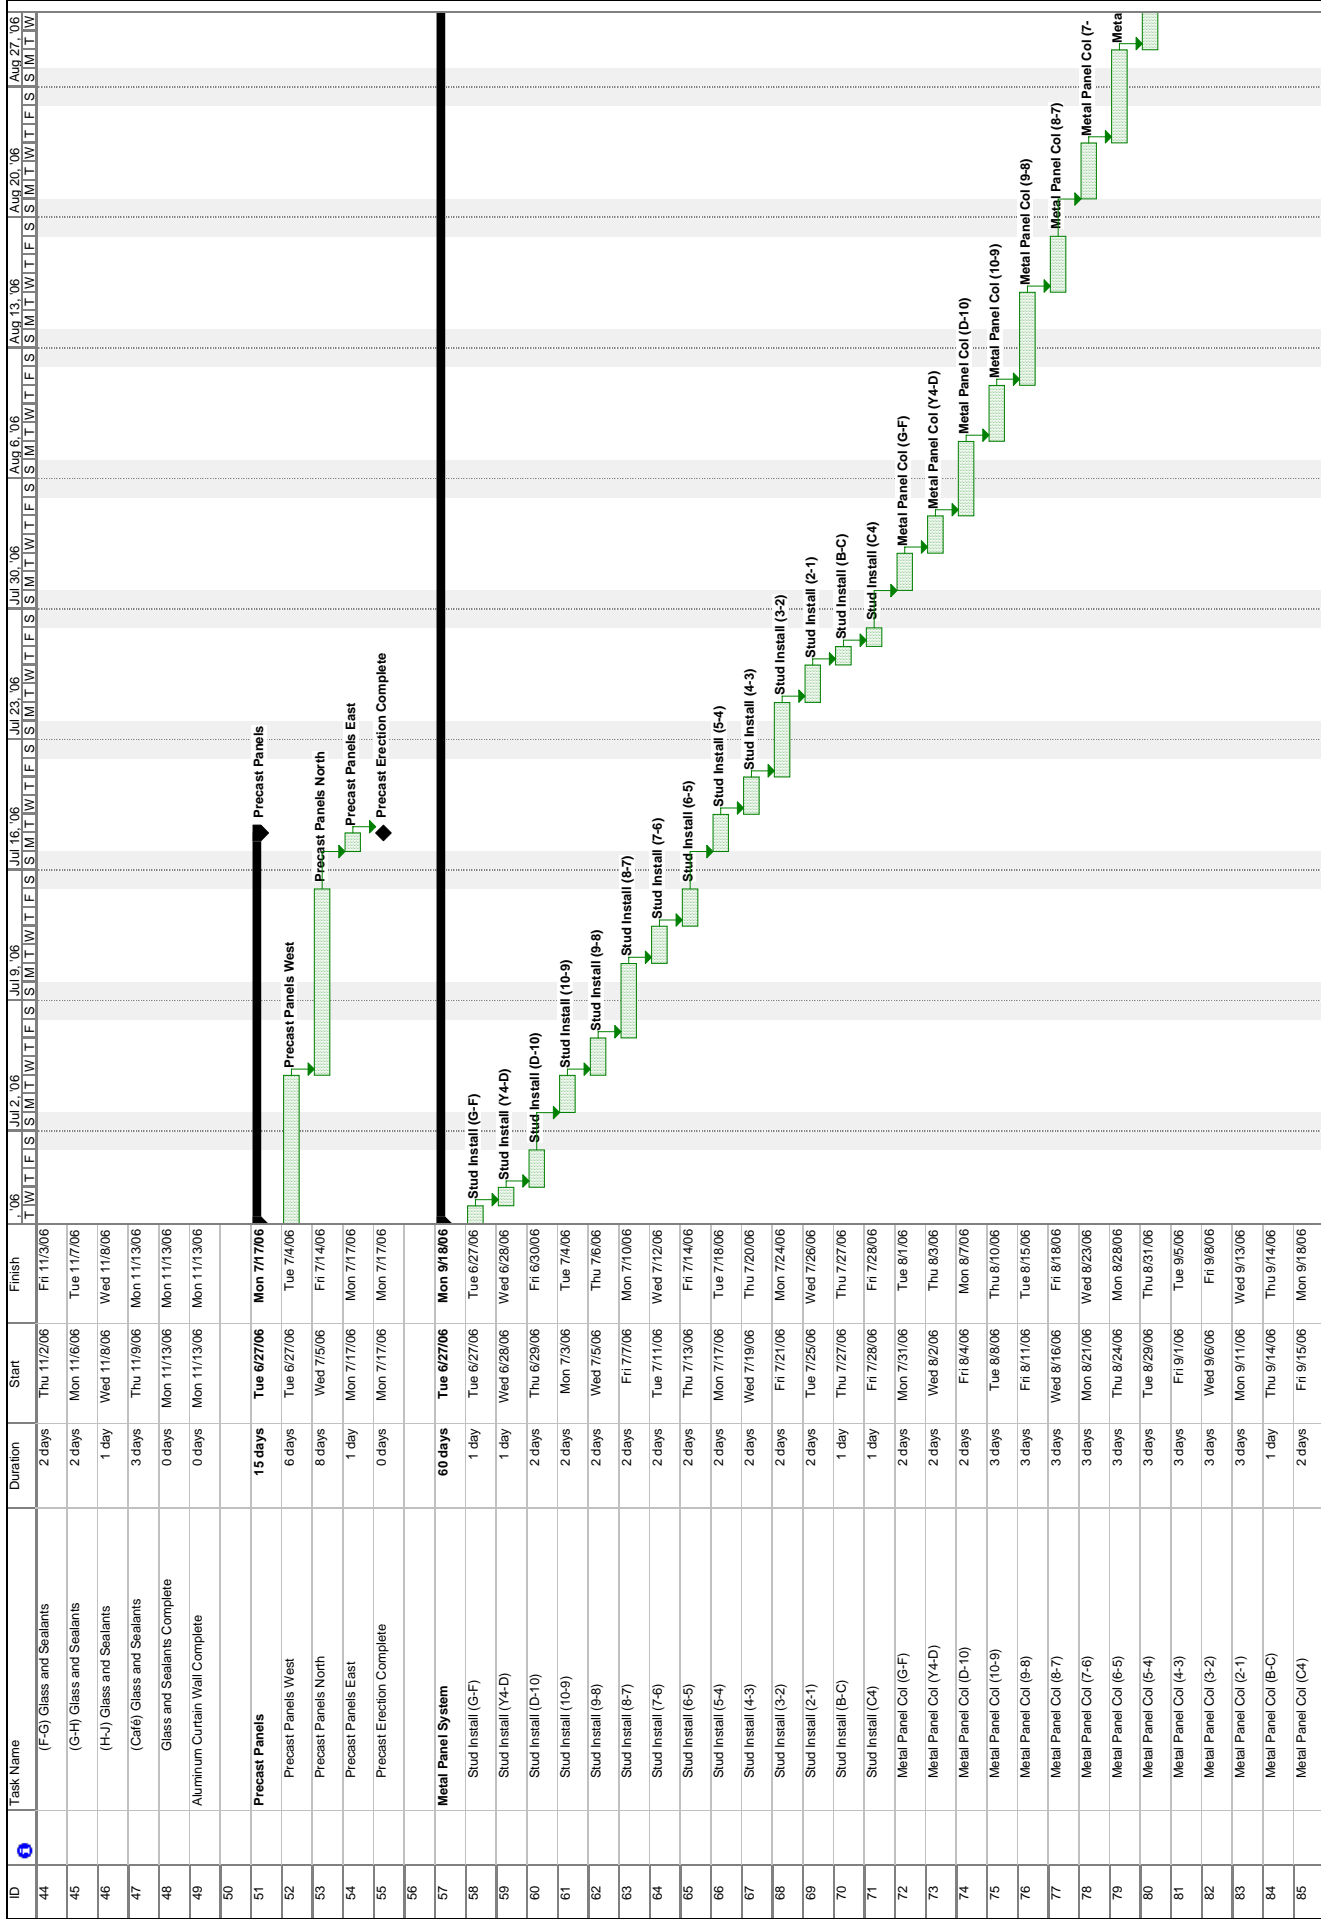

Project: Building Envelope Schedule
Date: Mon 4/3/06

Task: [Green bar] Progress: [Black bar]

Milestone: [Diamond symbol] Summary: [Black bar]

Rolled Up Task: [Green bar] Rolled Up Milestone: [Diamond symbol]

Rolled Up Progress: [Green bar] Split: [Vertical line]

External Tasks: [Grey bar] Project Summary: [Grey bar]

Group By Summary: [Black bar] Deadline: [Green arrow]

Page 2

ID	Task Name	Duration	Sep. 3, '06	Sep. 10, '06	Sep. 17, '06	Sep. 24, '06	Oct. 1, '06	Oct. 8, '06	Oct. 15, '06	Oct. 22, '06	Oct. 29, '06	Nov. 5, '06	Nov. 12, '06
44	(F-G) Glass and Sealants	2 days											
45	(G-H) Glass and Sealants	2 days											
46	(H-J) Glass and Sealants	1 day											
47	(Café) Glass and Sealants	3 days											
48	Glass and Sealants Complete	0 days											
49	Aluminum Curtain Wall Complete	0 days											
50													
51	Precast Panels	15 days											
52	Precast Panels West	6 days											
53	Precast Panels North	8 days											
54	Precast Panels East	1 day											
55	Precast Erection Complete	0 days											
56													
57	Metal Panel System	60 days											
58	Stud Install (G-F)	1 day											
59	Stud Install (Y4-D)	1 day											
60	Stud Install (D-10)	2 days											
61	Stud Install (10-9)	2 days											
62	Stud Install (9-8)	2 days											
63	Stud Install (8-7)	2 days											
64	Stud Install (7-6)	2 days											
65	Stud Install (6-5)	2 days											
66	Stud Install (5-4)	2 days											
67	Stud Install (4-3)	2 days											
68	Stud Install (3-2)	2 days											
69	Stud Install (2-1)	2 days											
70	Stud Install (B-C)	1 day											
71	Stud Install (C4)	1 day											
72	Metal Panel Col (G-F)	2 days											
73	Metal Panel Col (Y4-D)	2 days											
74	Metal Panel Col (D-10)	2 days											
75	Metal Panel Col (10-9)	3 days											
76	Metal Panel Col (9-8)	3 days											
77	Metal Panel Col (8-7)	3 days											
78	Metal Panel Col (7-6)	3 days											
79	Metal Panel Col (6-5)	3 days											
80	Metal Panel Col (5-4)	3 days											
81	Metal Panel Col (4-3)	3 days											
82	Metal Panel Col (3-2)	3 days											
83	Metal Panel Col (2-1)	3 days											
84	Metal Panel Col (B-C)	1 day											
85	Metal Panel Col (C4)	2 days											

Project: Building Envelope Schedule
Date: Mon 4/3/06

Task: [Green Bar] Progress: [Black Bar]

Milestone Summary: [Diamond]

Rolled Up Task: [Green Bar] Milestone Summary: [Diamond]

Rolled Up Progress: [Black Bar] Split: [Dotted Line]

External Tasks: [Grey Bar] Project Summary: [Grey Bar]

Group By Summary: [Arrow] Deadline: [Green Arrow]
