


Project: TECH2 SCHED
Date: Sun 10/29/06

Task Milestone Rolled Up Task Rolled Up Progress External Tasks Group By Summary
 Progress Summary Rolled Up Milestone Split Project Summary Deadline

ID	Task Name	Duration	Start	Finish	November 1		January 1		March 1		May 1		July 1		September 1		November 1		January 1		March 1	
					10/9	11/6	12/4	1/1	1/29	2/26	3/26	4/23	5/21	6/18	7/16	8/13	9/10	10/8	11/5	12/3	12/31	1/28
45	EXCAVATE/ INSTALL CONCRETE FOOTINGS	15 days	Mon 8/7/06	Fri 8/25/06																		
46	CONSTRUCT MASONRY BOAT STORAGE ENCLOSURE	30 days	Wed 8/16/06	Tue 9/26/06																		
47	COMPLETE ELECTRICAL SERVICE	5 days	Thu 9/14/06	Wed 9/20/06																		
48	INSTALL SITE LIGHTING	5 days	Thu 9/14/06	Wed 9/20/06																		
49	INSTALL WATER & SEWAR LINE	20 days	Thu 9/14/06	Wed 10/11/06																		
50	FOOTING & MASONRY WALL AT WATER LINE	15 days	Mon 10/9/06	Fri 10/27/06																		
51	PROVIDE ROAD CUTTING & FINAL GRADING	5 days	Thu 10/19/06	Wed 10/25/06																		
52	PAVING	5 days	Wed 10/25/06	Tue 10/31/06																		
53	INSTALL ENTRY GATES	5 days	Tue 10/31/06	Mon 11/6/06																		
54	LANDSCAPPING	5 days	Tue 10/31/06	Mon 11/6/06																		
55	BOAT STORAGE COMPLETED	0 days	Mon 11/6/06	Mon 11/6/06																		
56	DEMO-DEMOLITION	44 days	Mon 7/10/06	Thu 9/7/06																		
57	MOBILIZATION	0 days	Mon 7/10/06	Mon 7/10/06																		
58	SELECTIVE DEMOLITION	10 days	Mon 7/10/06	Fri 7/21/06																		
59	SAFE OFF RELOCATE EXISITING UTILITIES	10 days	Mon 7/10/06	Fri 7/21/06																		
60	CUT IN DOORS & SUPPORT STEEL @ TILT UP PANELS	10 days	Wed 7/12/06	Tue 7/25/06																		
61	FRAMING/ SHEATHING TEMP COORIDOR NORTH	15 days	Mon 7/17/06	Fri 8/4/06																		
62	FRAMING/ SHEATHING TEMP COORIDOR SOUTH	15 days	Mon 7/17/06	Fri 8/4/06																		
63	REMOVAL OF EXISTING SLAB, FOOTINGS & PILES	15 days	Mon 7/17/06	Fri 8/4/06																		
64	REMOVAL EXISTING UTILITIES & RTU 2A	5 days	Thu 7/20/06	Wed 7/26/06																		
65	ELECTRICAL/ FIRE ALARM IN NORTH COORIDOR	5 days	Mon 8/7/06	Fri 8/11/06																		
66	FIRE PROTECTION NORTH COORIDOR	5 days	Mon 8/7/06	Fri 8/11/06																		
67	ELECTRICAL/ FIRE ALARM IN SOUTH COORIDOR	5 days	Mon 8/7/06	Fri 8/11/06																		
68	FIRE PROTECTION SOUTH COORIDOR	5 days	Mon 8/7/06	Fri 8/11/06																		
69	DEMOLITION OF EXISITING EXTERIOR SHELL	15 days	Mon 8/21/06	Fri 9/8/06																		
70	CUT BACK EXISITING ROOFING	10 days	Mon 8/28/06	Fri 9/8/06																		
71	TEMPORARY PROTECTION EXISITING MALL EXTERIOR	10 days	Mon 8/28/06	Fri 9/8/06																		
72	TEMPORARY EXTERIOR WALL AT COURT #1	10 days	Mon 8/28/06	Fri 9/8/06																		
73	MC-MALL RECONFIGURATION	95 days	Mon 7/24/06	Fri 12/1/06																		
74	EXCAVATIONS FOR FOOTINGS & FOUNDATION	10 days	Mon 7/24/06	Fri 8/4/06																		
75	INSTALL MASONRY WALL, COLUMN FOOTINGS & SLAB	10 days	Thu 8/3/06	Wed 8/16/06																		
76	CONSTRUCT NEW MASONRY DEMISING PARTITION	30 days	Mon 8/28/06	Fri 10/6/06																		
77	ERECTION OF NEW STRUCTURAL STEEL & ROOF DECKING	15 days	Mon 9/25/06	Fri 10/13/06																		
78	RELOCATION/ ADDITION OF ROOF DRAINAGE	10 days	Thu 10/12/06	Wed 10/25/06																		
79	INSTALL NEW ROOFING	15 days	Thu 10/12/06	Wed 11/1/06																		
80	ROOF TIE IN AT EXTERIOR WALL	5 days	Tue 10/24/06	Mon 10/30/06																		
81	EXTERIOR FINISH OF MASONRY PARTITION	5 days	Mon 10/30/06	Fri 11/3/06																		
82	RELOCATION OF RTU 2A	5 days	Mon 10/30/06	Fri 11/3/06																		
83	CONSTRUCT BULK HEAD PARTITION	10 days	Mon 10/30/06	Fri 11/10/06																		
84	CONSTRUCT NEW DRYWALL COORIDOR PARTITION	15 days	Mon 10/30/06	Fri 11/17/06																		
85	INSTALL NEW ROOF TOP UNIT RT2B	5 days	Wed 11/1/06	Tue 11/7/06																		
86	INSTALL NEW SPRINKLER SYSTEM	10 days	Mon 11/6/06	Fri 11/17/06																		
87	INSTALL LIGHTING & FIRE ALARM IN NEW COORIDOR	10 days	Mon 11/6/06	Fri 11/17/06																		
88	EXTEND HVAC SYSTEM	5 days	Fri 11/10/06	Thu 11/16/06																		

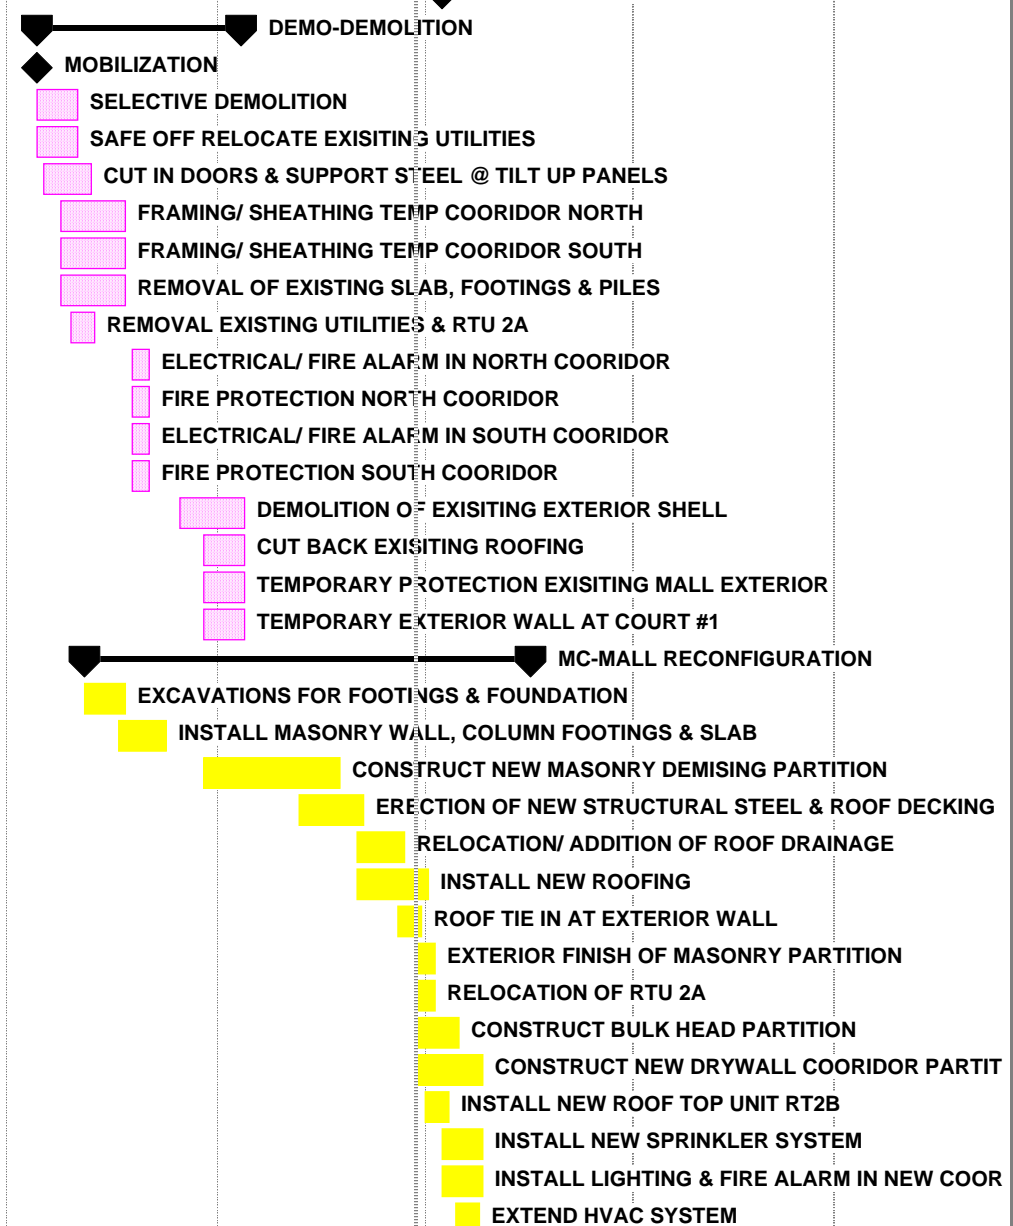


Project: TECH2 SCHED Date: Sun 10/29/06

Task: [Blue Bar] Milestone: [Diamond] Rolled Up Task: [Blue Bar] Rolled Up Progress: [Thick Black Bar] External Tasks: [Grey Bar] Group By Summary: [Thick Black Bar]

Progress: [Thick Black Bar] Summary: [Thick Black Bar] Rolled Up Milestone: [Diamond] Split: [Dotted Blue Bar] Project Summary: [Grey Bar] Deadline: [Green Arrow]

ID	Task Name	Duration	Start	Finish	November 1			January 1		March 1		May 1		July 1			September 1		November 1		January 1		March 1	
					10/9	11/6	12/4	1/1	1/29	2/26	3/26	4/23	5/21	6/18	7/16	8/13	9/10	10/8	11/5	12/3	12/31	1/28	2/25	3/25
89	COLOT CONCRETE FLOORING AT ENTRY #1	2 days	Tue 10/10/06	Wed 10/11/06																				
90	FINISH CORRIDOR WALLS	5 days	Mon 11/13/06	Fri 11/17/06																				
91	INSTALL SIGNAGE	2 days	Tue 11/14/06	Wed 11/15/06																				
92	RECEIVE CERTIFICATE OF OCCUPANCY	0 days	Fri 11/17/06	Fri 11/17/06																				
93	REMOVE TEMPORARY PEDESTRIAN CORRIDORS	10 days	Mon 11/20/06	Fri 12/1/06																				
94	TEMPORARY PARTITIONS AT ENTRY #1	5 days	Mon 11/27/06	Fri 12/1/06																				
95	INSTALL DOORS & HW AT CORRIDOR AND PARTITION	2 days	Thu 11/30/06	Fri 12/1/06																				
96	COMPLETION OF MALL RECONFIGURATION	0 days	Fri 12/1/06	Fri 12/1/06																				
97	ID-INFORMATION DESK RELOCATION	15 days	Mon 8/28/06	Fri 9/15/06																				
98	RELOCATION OF ELECTRICAL/ TELCOM COURT #2	6 days	Mon 8/28/06	Mon 9/4/06																				
99	PATCH EXISITING CONCRETE SLAB & STAIN	2 days	Mon 9/4/06	Tue 9/5/06																				
100	DISASSEMBLE EXISITING INFO DESK AT COURT #1	5 days	Wed 9/6/06	Tue 9/12/06																				
101	REINSTALL INFO DESK AT COURT #2	5 days	Tue 9/12/06	Mon 9/18/06																				
102	CONSTRUCT TEMPORARY PARTITION AT ENTRY #1	3 days	Tue 9/12/06	Thu 9/14/06																				
103	FINAL CONNECTIONS/ MOVE IN	2 days	Mon 9/18/06	Tue 9/19/06																				
104	COMPLETE RELOCATION OF INFO DESK	0 days	Fri 10/27/06	Fri 10/27/06																				

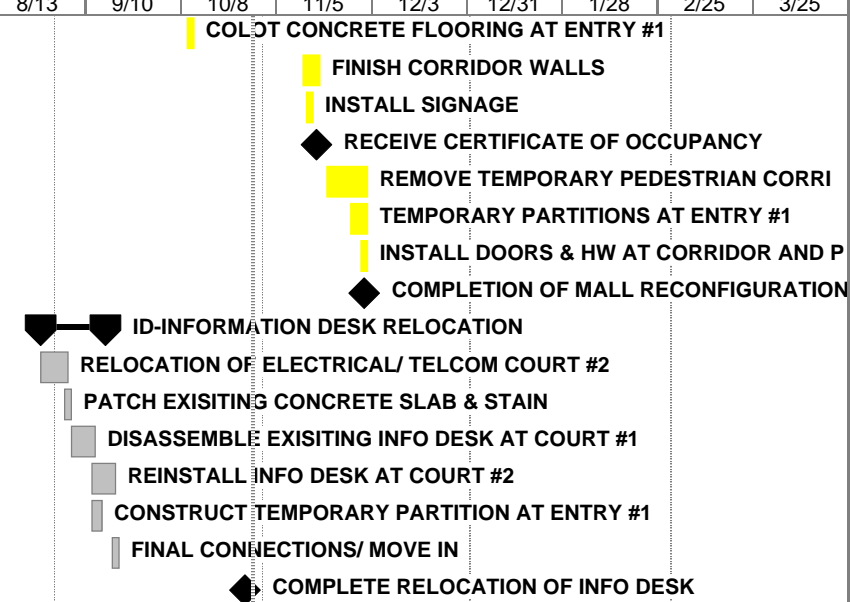

Project: TECH2 SCHED
Date: Sun 10/29/06

Task Milestone Rolled Up Task Rolled Up Progress External Tasks Group By Summary

Progress Summary Rolled Up Milestone Split Project Summary Deadline
